


Apr-26: Technical Performance & Loss Analysis Report

This report presents a detailed, waterfall-based performance analysis for all solar PV sites in the portfolio for **April-26**. The purpose is to quantify the contribution of key factors—radiation, temperature, array performance, inverter efficiency, AC losses, plant breakdown, curtailment, and unforeseen losses—to the deviation between budgeted and actual energy generation.

Each site includes the following visualizations:

1. Portfolio Overview
2. Plant Performance Vitals
3. Action Taken Report
4. Budget vs Actual Generation Delta Waterfall
5. Actual Loss Breakdown Waterfall
6. Inverter Performance Report
7. String Performance Report

Sequence in the report is as follows:



Note: 1. Curtailment loss units are tentative; actual numbers will be reconciled monthly.


1. Portfolio Overview

Site	Generation(MWh)			GTI(kWh/m ²)		Plant losses(MWh)	Grid+Curtailment losses(MWh)	Plant Availability %	PR%	
	Budget	Weather Corrected Budget	Actual	Budget	Actual				Budget	Actual
Groensebos	1,624	1,905	↓ 1,307	133	↑ 152	-1	-431	100%	92%	↓ 64%
Echt	605	750	↓ 582	134	↑ 162	-36	-52	↓ 94%	89%	↓ 70%
Venray	373	471	↑ 387	134	↑ 167	0	-24	100%	77%	↓ 66%
Tinte	1,410	1,616	↓ 1,343	143	↑ 161	↓ -90	-148	↓ 94%	72%	↓ 66%
Snelle loop	3,653	3,875	↓ 2,444	159	↑ 162	-15	0	99%	86%	↓ 56%
NOP Midden	2,015	2,047	↓ 26	149	↓ 148	0	-665	100%	85%	↓ 1%
NOP Noord	3,260	3,365	↓ 35	149	↑ 151	↓ -75	-1032	↓ 32%	86%	↓ 1%
NOP Plot4	1,860	1,914	↓ 20	149	↑ 150	0	-594	100%	87%	↓ 1%
NOP Zuid	5,182	5,380	↓ 25	149	↑ 152	0	-1661	100%	87%	↓ 0%
Gorgast Bahn	2,006	2,135	↓ 457	154	↑ 157	↓ -222	-451	↓ 67%	88%	↓ 19%
Gorgast Gewachshaus	1,683	1,646	↓ 923	147	↓ 136	-23	-1297	98%	81%	↓ 47%
Gorgast Manschnow	1,827	1,877	↓ 406	146	↓ 143	-3	-441	99%	80%	↓ 18%
Edinburgh	1,157	1,303	↓ 875	128	↑ 140	-4	-287	100%	90%	↓ 64%
Northwold	1,379	1,615	↑ 1,436	151	↑ 171	↓ -64	0	96%	92%	↓ 84%
Portfolio	28,034	29,901	↓ 10,267	2,023	↑ 2,153	-532	-7084	95%	86%	↓ 30%

Performance Analysis Report: Portfolio

AC Capacity (MW): 158 MW DC Capacity (MWp): 222 MWp

MTD Report: Portfolio

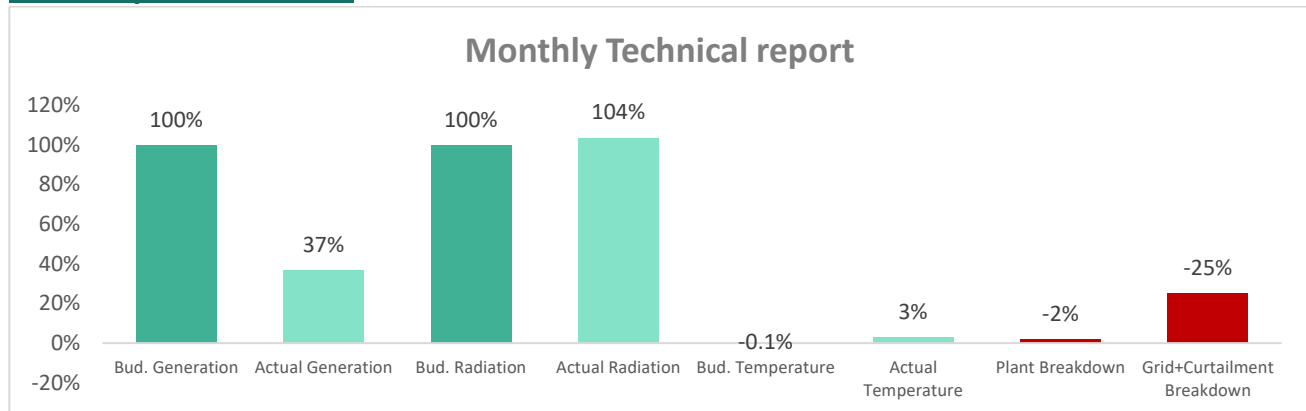

Month	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MW h)	Actual Temperature Factor(MW h)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)
Apr-26	28,034	10,267	147	153	-27	999	-532	-7,084
	100.0%	36.6%	100.0%	103.6%	-0.1%	2.9%	-1.9%	-25.3%

From the above graph it is clearly visible that the Actual Generation achieved 36.6% of Budgeted Generation, Actual Radiation is 103.6% of Budgeted Radiation.

Action Taken Report: Portfolio

8

Critical Issues Identified

525


MWh Generation Loss

86%

Closed (7 of 8)

Issue	Site	Category	Loss(MWh)	Date	Root Cause	Status	Remarks
1.	Northwold	Outage	64	29-04-2026	Plant outage happened at site. Issue Days: 2	Completed	As per Mettlen there was controller issue at site
2.	Tinte	Cable Theft	90	01-04-2026	Cable Theft at site. Issue Days: 16	WIP	Theft 1 restored on 15 th Apr, Theft 2 occurred on 30 th Apr
3.	Echt	Transformer	36	11-04-2026	LV side smoke detector operated Issue Days: 2	Completed	
4.	NOP Noord	Communication		01-04-2026	Communication issue between SunGrow logger and VCOM. Issue Days: 14	Completed	
5.	NOP Noord	Inverter Fault	75	04-04-2026	Inverter Fuailt . Issue Days: 28	Completed	
6.	Snelle loop	Shutdown	15	02-04-2026	Shutdown due to testing and technical issues Issue Days: 1	Completed	
7.	Gorgast Bahn	Communication	222	01-02-2026	Communication issue due to replacement of relays, inverters were not producing Issue Days: 27	Completed	
8.	Gorgast Gewachshaus	Inverter Fault	23	26-03-2026	Inverter under breakdown due to Internal Fault Issue Days: 17	Completed	Inverter replaced and restored on 17 th Apr
TOTAL			525 MWh				


Budget Vs Actual: Portfolio

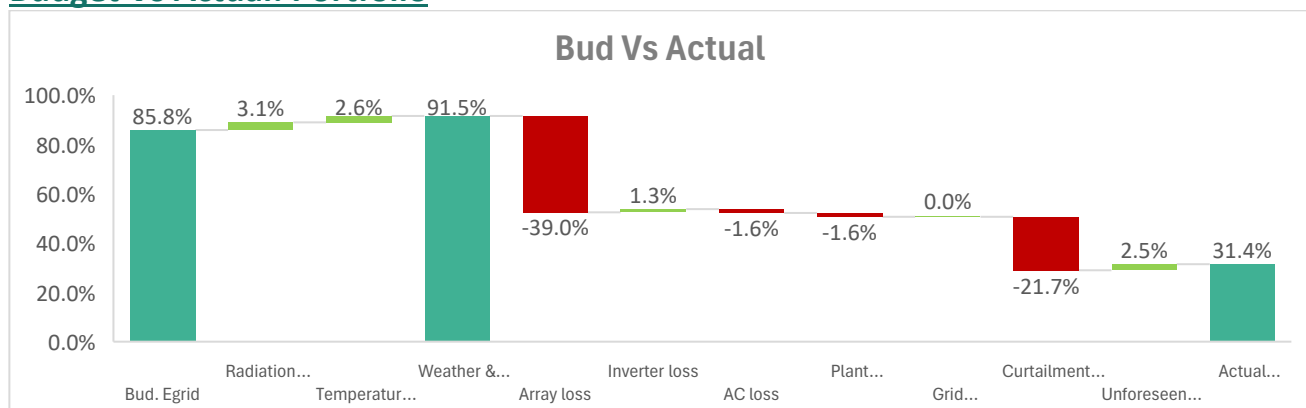

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtilment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	32,684	28,034	1,019	877	29,903	-12,756	433	-384	-532.1	-7,084	817	10,267
	100.0%	85.8%	3.1%	2.6%	91.5%	-39.0%	1.3%	-1.6%	-1.6%	-21.7%	2.5%	31.4%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, Plant and Grid & Curtailment breakdowns are seen, accounting for most of the technical reduction. Temperature factor and Radiation are contributing more than their budgeted numbers. Overall, 31.4% of actual generation is achieved of budgeted max theoretical numbers.

MTD Actual Losses Report: Portfolio

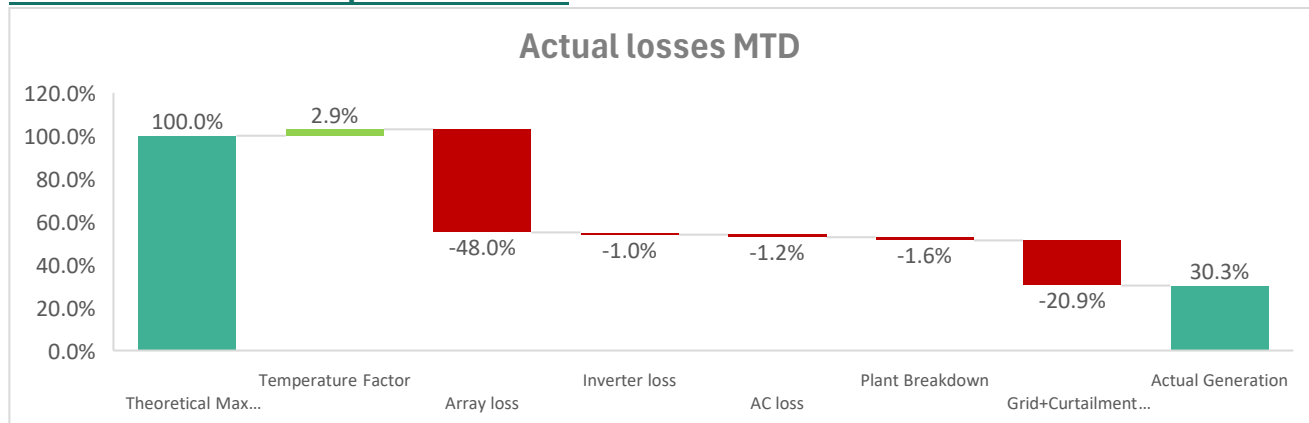


Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtilment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	33871	999	-16251	-335	-401	-532	-7084	10267
	100.0%	2.9%	-48.0%	-1.0%	-1.2%	-1.6%	-20.9%	30.3%

From the Theoretical Max generation baseline an Array, Plant and Grid & Curtailment breakdown losses are seen, accounting for most of the technical reduction. Overall, 30.3% of actual generation is achieved of theoretical max numbers.

2. Performance Analysis Report: Groensebos

AC Capacity (MW): 10 MW DC Capacity (MWp): 13.3 MWp Location: NL


MTD Report: Groensebos

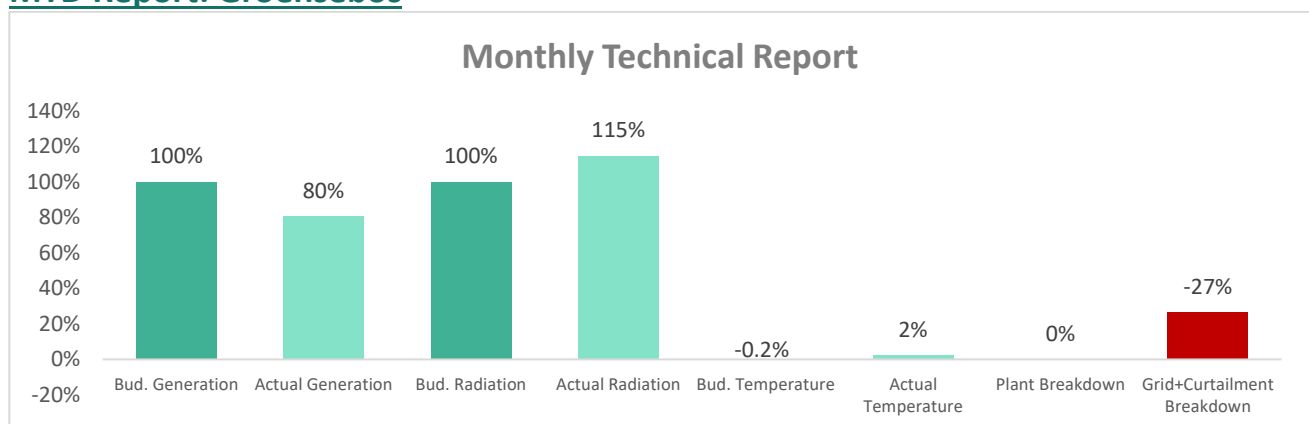

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)
Apr-26	1,624	1,307	133	152	-4	46	-1	-431
	100.0%	80.5%	100.0%	114.7%	-0.2%	2.3%	-0.1%	-26.5%

From the above graph it is clearly visible that the Actual Generation achieved 80.5% of Budgeted Generation, Actual Radiation is 114.7% of Budgeted Radiation.


Budget Vs Actual Comparison: Groensebos

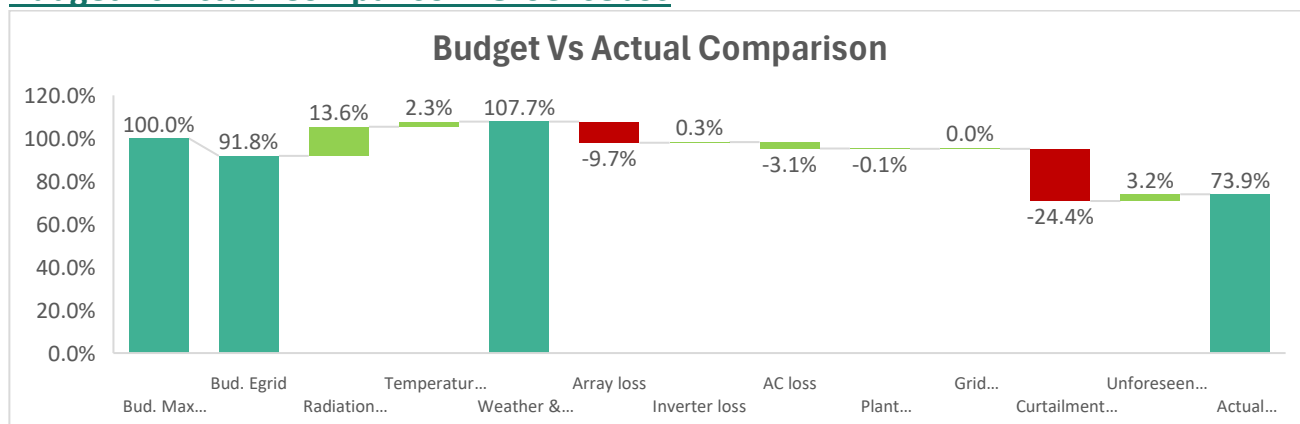

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	1,769	1,624	240	44	1,905	-172	5	-47	-1.2	-431	56	1,307
	100.0%	91.8%	13.6%	2.3%	107.7%	-9.7%	0.3%	-3.1%	-0.1%	-24.4%	3.2%	73.9%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Grid & Curtailment breakdowns are seen, accounting for most of the technical reduction. Temperature factor and Radiation losses are contributing more than their budgeted numbers. Overall, 73.9% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Groensebos

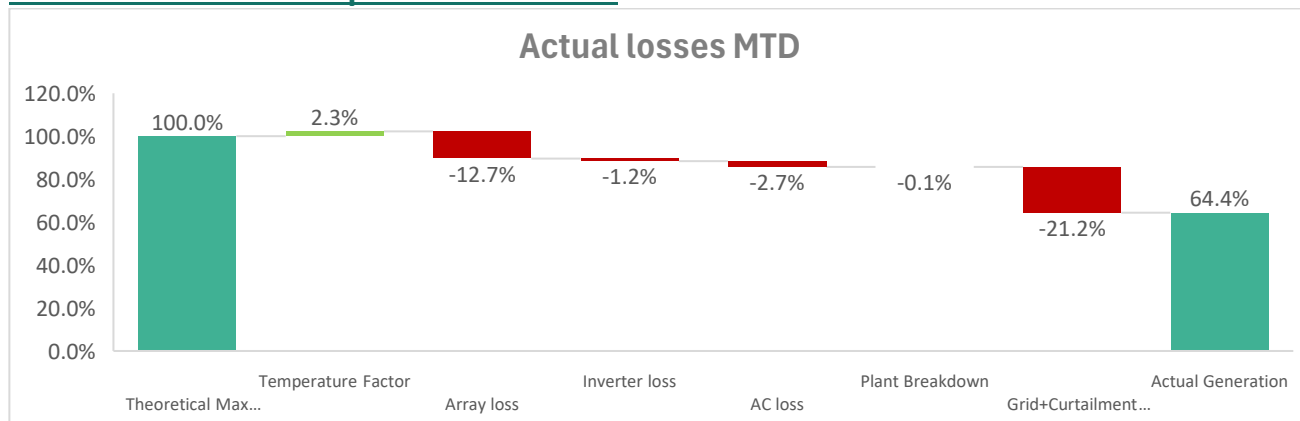

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2029	46	-257	-25	-54	-1	-431	1307
	100.0%	2.3%	-12.7%	-1.2%	-2.7%	-0.1%	-21.2%	64.4%

From the Theoretical Max generation baseline an Array, AC and Grid & Curtailment breakdown losses are seen, accounting for most of the technical reduction. Overall, 64.4% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Groensebos

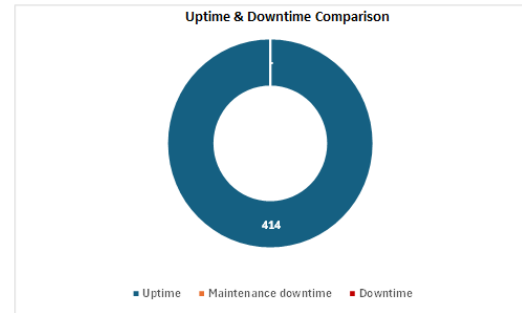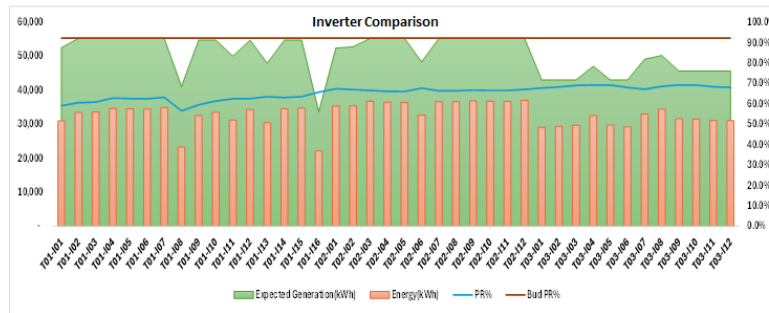

Top 5 Inverters

Inverter Name	PR%	Yield
T03-I03	68.9%	105.1
T03-I04	69.1%	105.3
T03-I05	69.0%	105.3
T03-I09	69.1%	105.4
T03-I11	68.2%	104.1

Bottom 5 Inverters

Inverter Name	PR%	Yield
T01-I01	59.0%	89.9
T01-I08	56.5%	86.1
T01-I09	59.4%	90.6

Downtime Details

1. Maintenance: NA
2. Downtime: NA

String Performance Report: Groensebos

Total Strings: 459
Normal Strings: 403
Underperforming Strings Z-Score<-1: 38
Faulty Strings Z-Score<-2: 10
Severe Strings Z-Score<-3: 8

Underperforming Strings	Deviation%	Severe Strings	Deviation%
T1.14-DC4_1	-2.5%	T1.10-DC11_1	-100.0%
T1.14-DC6_1	-3.6%	T3.12-DC1_1	-100.0%
T1.13-DC5_1	-4.2%	T3.12-DC10_1	-100.0%
T1.13-DC7_1	-2.9%	T3.12-DC2_1	-100.0%
T1.15-DC12_1	-3.4%	T3.12-DC3_1	-100.0%


3. Performance Analysis Report: Echt

AC Capacity (MW): 4 MW

DC Capacity (MWp): 5.1 MWp

Location: NL


MTD Report: Echt

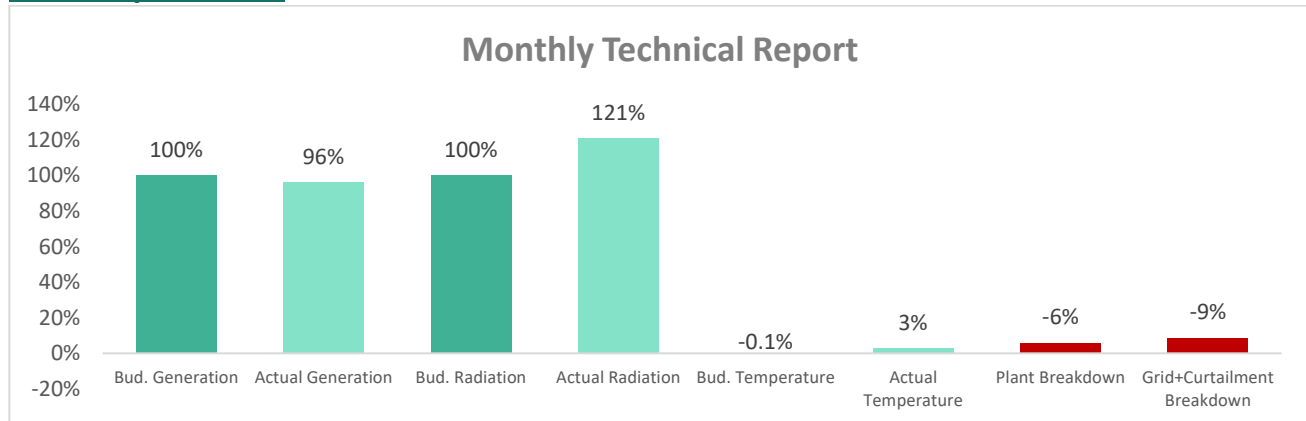

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)
Apr-26	605	582	134	162	-1	22	-36	-52
	100.0%	96.2%	100.0%	121.0%	-0.1%	2.6%	-5.9%	-8.7%

From the above graph it is clearly visible that the Actual Generation achieved 96.2% of Budgeted Generation, Actual Radiation is 121.0% of Budgeted Radiation.


Budget Vs Actual Comparison: Echt

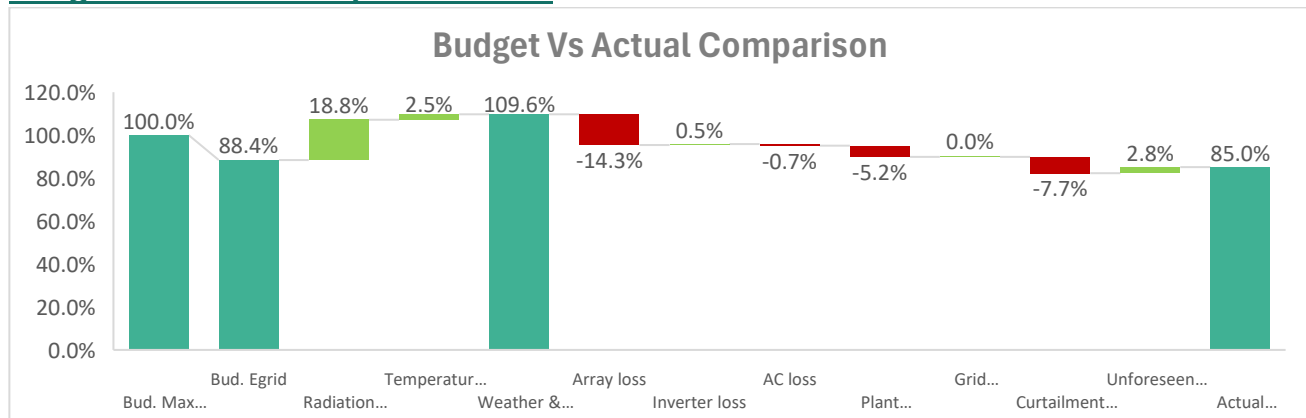

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	685	605	128	18	750	-98	3	-4	-36	-52	19	582
	100.0%	88.4%	18.8%	2.5%	109.6%	-14.3%	0.5%	-0.7%	-5.2%	-7.7%	2.8%	85.0%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array losses, Plant and Grid & Curtailement losses account for most of the technical reduction. Radiation and temperature loss are contributing more than their budgeted numbers. Overall, 85.0% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Echt

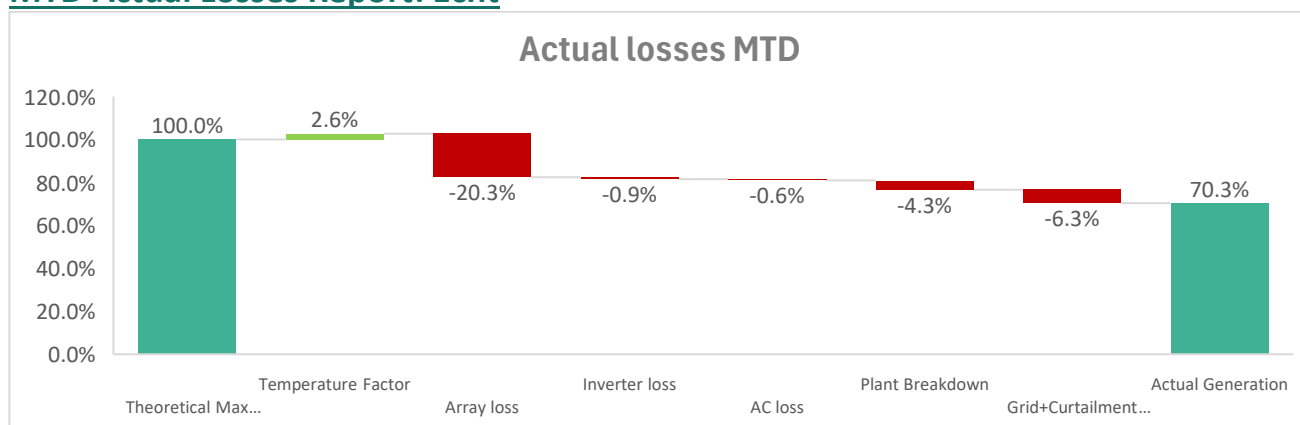

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Actual Generation (MWh)
Apr-26	828	22	-168	-7	-5	-36	-52	582
	100.0%	2.6%	-20.3%	-0.9%	-0.6%	-4.3%	-6.3%	70.3%

From the Theoretical Max generation baseline an Array loss, Plant and Grid & curtailment losses are seen, accounting for most of the technical reduction. Overall, 70.3% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Echt

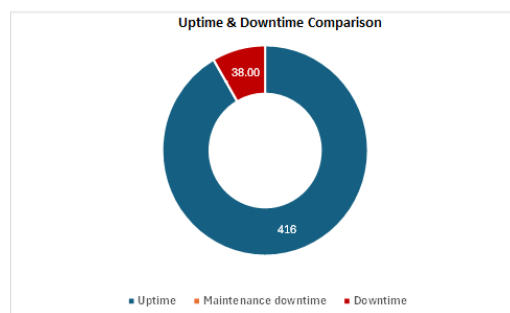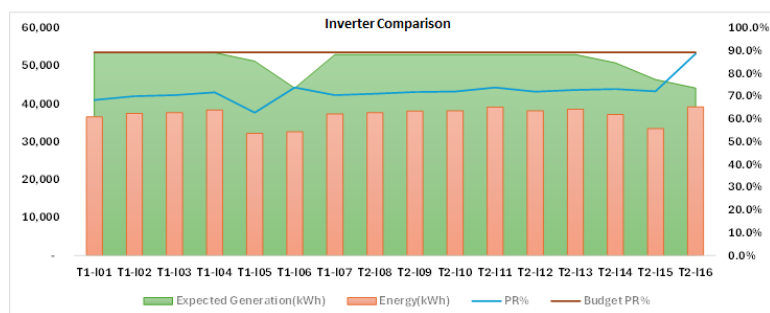

Top 5 Inverters

Inverter Name	PR%	Yield
T1-I06	73.9%	119.2
T2-I10	72.1%	116.4
T2-I11	73.8%	119.2
T2-I14	73.2%	118.2
T2-I16	88.7%	143.2

Bottom 5 Inverters

Inverter Name	PR%	Yield
T1-I01	68.3%	110.3
T1-I05	62.8%	101.4

Downtime Details

1. Maintenance: NA
2. Downtime: 2 days
Impact: 2.3

String Performance Report: Echt


Total Strings: 371
Normal Strings: 303
Underperforming Strings Z-Score<-1: 66
Faulty Strings Z-Score<-2: 2
Severe Strings Z-Score<-3: 0

Underperforming Strings	Deviation%	Faulty Strings	Deviation%
INV01- String-13	-4.3%	INV01- String-12	-8.1%
INV05- String-11	-4.5%	INV16- String-17	-7.9%
INV05- String-14	-4.7%		
INV07- String-06	-3.9%		
INV10- String-15	-3.9%		

4. Performance Analysis Report: Venray

AC Capacity (MW): 3.5 MW DC Capacity (MWp): 2.5 MWp Location: NL


MTD Report: Venray

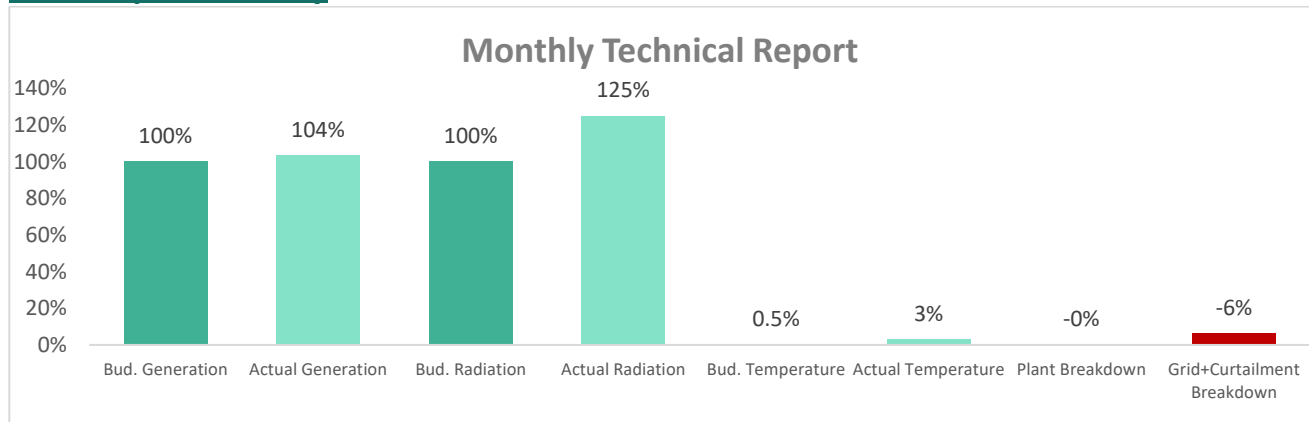

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MW h)	Actual Temperature Factor(MW h)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)
Apr-26	373	387	134	167	2	17	-	-24
	100.0%	103.7%	100.0%	125.0%	0.5%	2.8%	0.0%	6.4%

From the above graph it is clearly visible that the Actual Generation achieved 103.7% of Budgeted Generation, Actual Radiation is 125.0% of Budgeted Radiation.


Budget Vs Actual Comparison: Venray

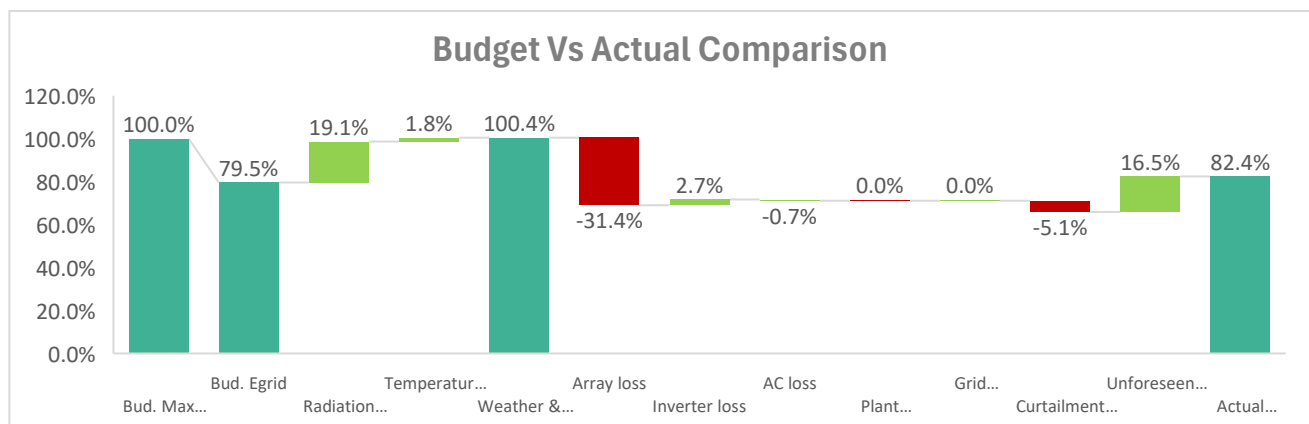

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid (MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid (MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	469	373	90	6	471	-147	12	-3	-	-24	78	387
	100.0%	79.5%	19.1%	1.8%	100.4%	-31.4%	2.7%	-0.7%	0.0%	-5.1%	16.5%	82.4%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Grid & Curtailment losses account for most of the technical reduction. Radiation, Temperature, Inverter losses are contributing more than their budgeted numbers. Overall, 82.4% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Venray

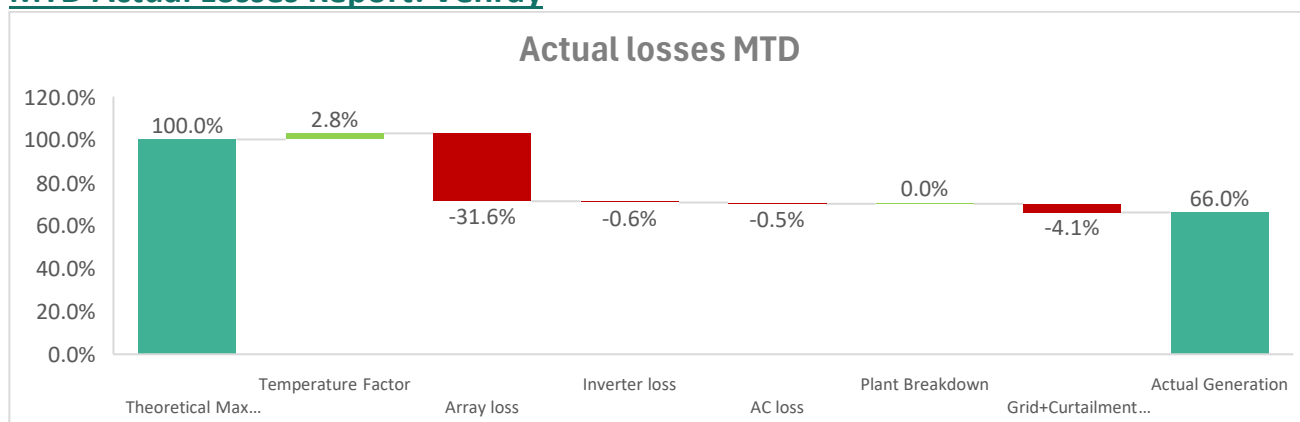

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Actual Generation (MWh)
Apr-26	586	17	-185	-4	-3	0	-24	387
	100.0%	2.8%	-31.6%	-0.6%	-0.5%	0.0%	-4.1%	66.0%

From the Theoretical Max generation baseline an Array loss and Grid & Curtailment losses are seen, accounting for most of the technical reduction. Overall, 66.0% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Venray

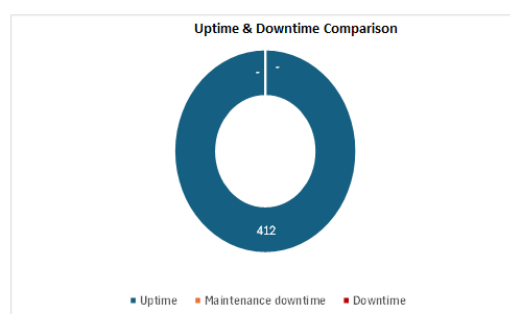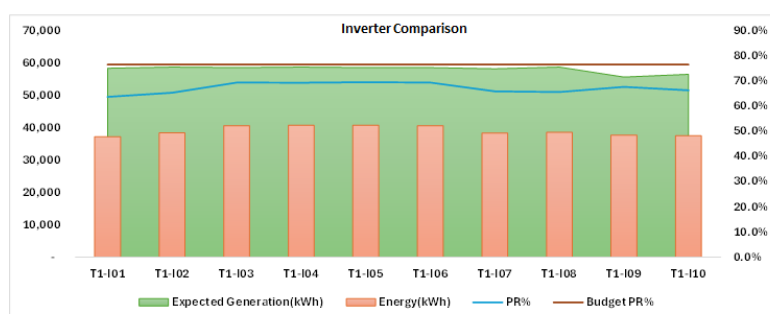

Top 5 Inverters

Inverter Name	PR%	Yield
T1-I03	69.4%	115.7
T1-I04	69.3%	115.6
T1-I05	69.5%	115.9
T1-I06	69.4%	115.7

Bottom 5 Inverters

Inverter Name	PR%	Yield
T1-I01	63.7%	106.2

Downtime Details

1. Maintenance: NA
2. Downtime: NA

String Performance Report: Venray


Total Strings: 239
Normal Strings: 197
Underperforming Strings Z-Score<-1: 32
Faulty Strings Z-Score<-2: 7
Severe Strings Z-Score<-3: 3

Underperforming Strings	Deviation%	Faulty Strings	Deviation%
Inverter 02.DC10	-2.3%	Inverter 01.DC5	-20.3%
Inverter 02.DC2	-2.7%	Inverter 01.DC6	-21.0%
Inverter 02.DC24	-2.6%	Inverter 03.DC1	-12.0%
Inverter 02.DC6	-2.3%	Inverter 03.DC2	-10.3%
Inverter 02.DC7	-2.8%	Inverter 05.DC23	-11.8%

5. Performance Analysis Report: Tinte

AC Capacity (MW): 9.8 MW DC Capacity (MWp): 12.6 MWp Location: NL


MTD Report: Tinte

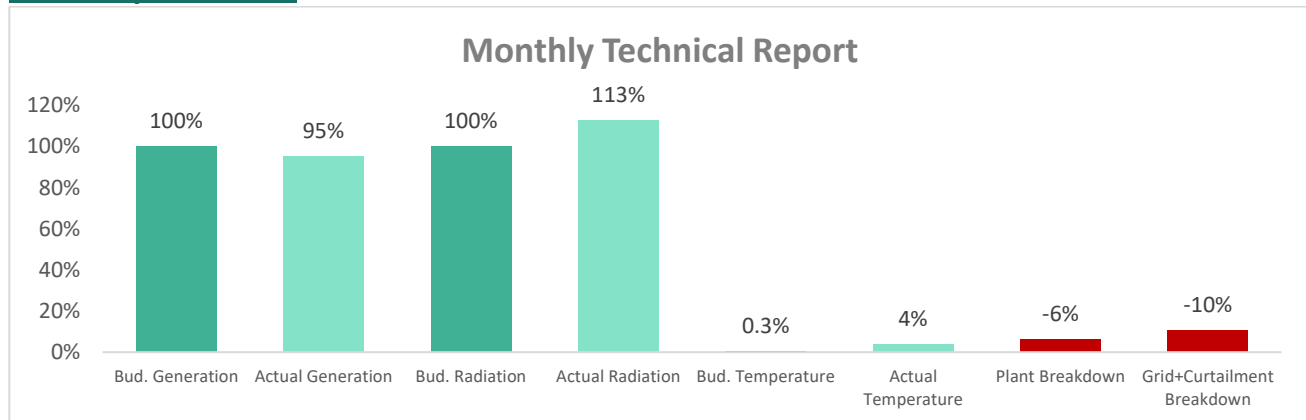

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)
Apr-26	1,410	1,343	143	161	6	73	-90	-148
	100.0%	95.2%	100.0%	112.7%	0.3%	3.6%	6.4%	10.5%

From the above graph it is clearly visible that the Actual Generation achieved 95.2% of Budgeted Generation, Actual Radiation is 112.7% of Budgeted Radiation.


Budget Vs Actual Comparison: Tinte

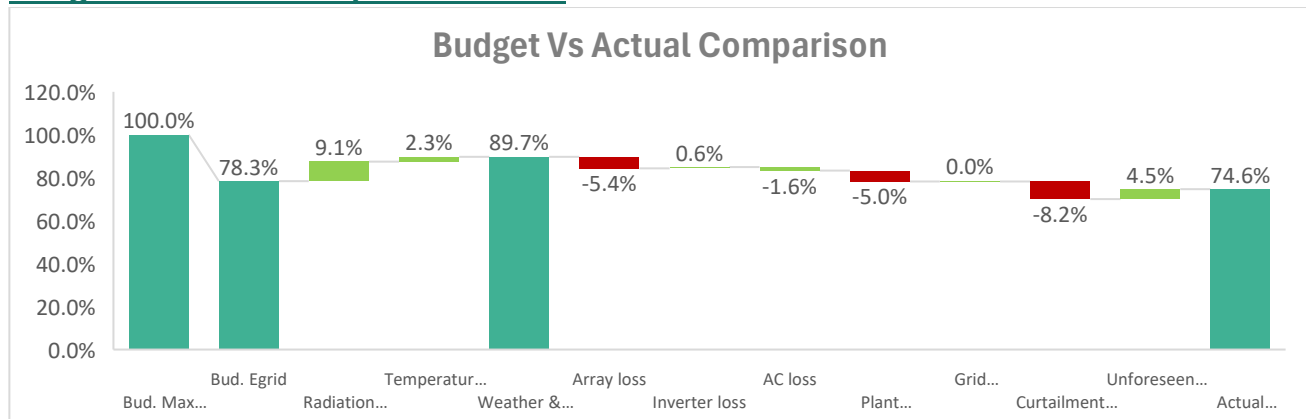

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	1,801	1,410	164	36	1,616	-97	10	-26	-90.2	-148	81	1,343
	100.0%	78.3%	9.1%	2.3%	89.7%	-5.4%	0.6%	-1.6%	-5.0%	-8.2%	4.5%	74.6%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, AC, Plant and Grid & Curtailment losses are seen, accounting for most of the technical reductions. Temperature, Radiation and Inverter losses are contributing more than their budgeted numbers. Overall, 74.6% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Tinte

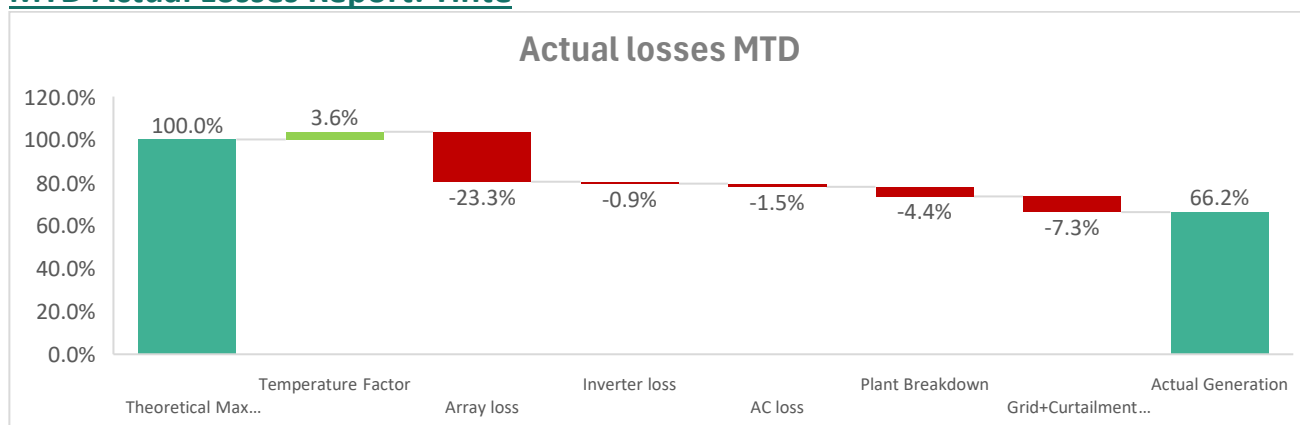

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2029	73	-473	-18	-30	-90	-148	1343
	100.0%	3.6%	-23.3%	-0.9%	-1.5%	-4.4%	-7.3%	66.2%

From the Theoretical Max generation baseline an Array, AC, Plant and Grid & curtailment breakdown losses are seen accounting for most of the technical reduction. Overall, 66.2% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Tinte

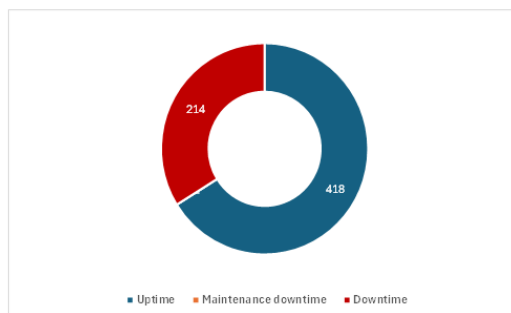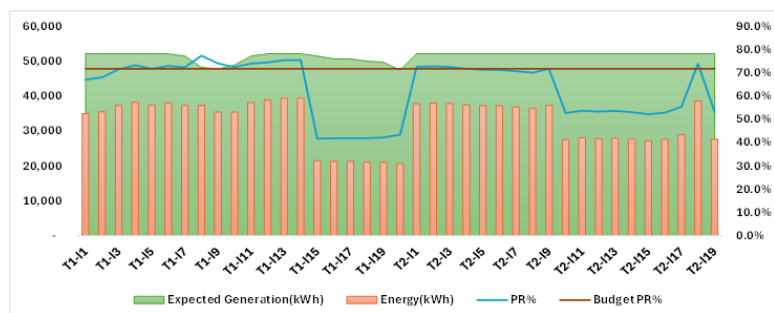

Top 5 Inverters

Inverter Name	PR%	Yield
T1-I8	77.4%	124.3
T1-I9	74.2%	119.0
T1-I12	74.6%	119.8
T1-I13	75.6%	121.3
T1-I14	75.6%	121.4

Bottom 5 Inverters

Inverter Name	PR%	Yield
T1-I15	41.7%	67.0
T1-I16	41.9%	67.2
T1-I17	41.9%	67.3
T1-I18	42.0%	67.4
T1-I19	42.3%	67.8

Downtime Details

1. Maintenance: NA
2. Downtime: 16 days, Impact: 90.2MWh

String Performance Report: Tinte


Total Strings:	935
Normal Strings:	774
Underperforming Strings Z-Score<-1:	143
Faulty Strings Z-Score<-2:	17
Severe Strings Z-Score<-3:	1

Underperforming Strings	Deviation%	Faulty Strings	Deviation%
Inverter 1.10.DC16	-4.3%	Inverter 1.15.DC13	-11.5%
Inverter 1.10.DC19	-3.2%	Inverter 1.15.DC14	-12.9%
Inverter 1.10.DC2	-3.9%	Inverter 1.16.DC18	-12.4%
Inverter 1.10.DC6	-3.8%	Inverter 1.17.DC12	-13.7%
Inverter 1.2.DC1	-4.8%	Inverter 1.18.DC4	-21.5%

6. Performance Analysis Report: NOP Midden

AC Capacity (MW): 10.3 MW DC Capacity (MWp): 15.9 MWp Location: NL


MTD Report: NOP Midden

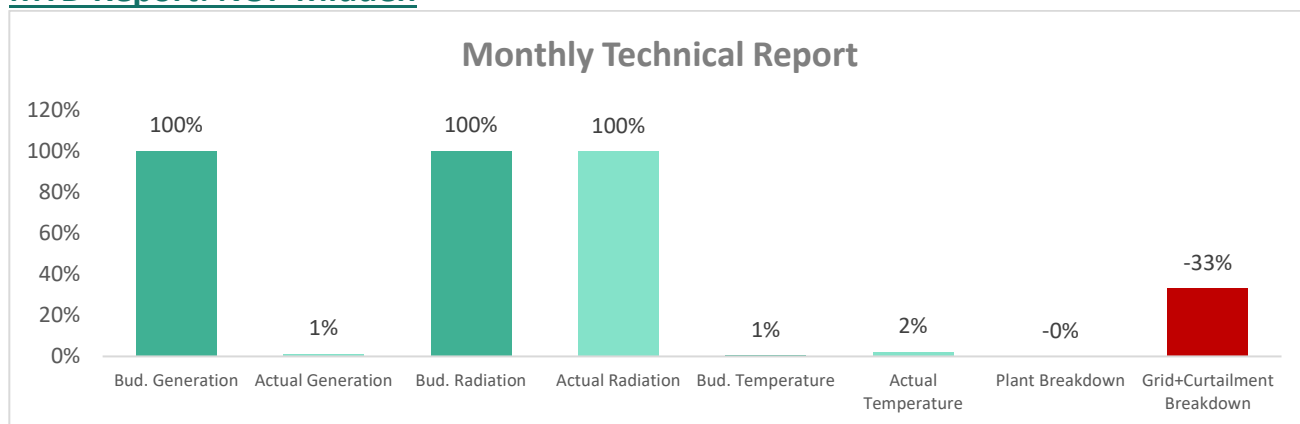

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	2,015	26	149	148	12	55	-	-665
	100.0%	1.3%	100.0%	99.8%	0.5%	2.3%	0.0%	33.0%

From the above graph it is clearly visible that the Actual Generation achieved 1.3% of Budgeted Generation, Actual Radiation is 99.8% of Budgeted Radiation.


Budget Vs Actual Comparison: NOP Midden

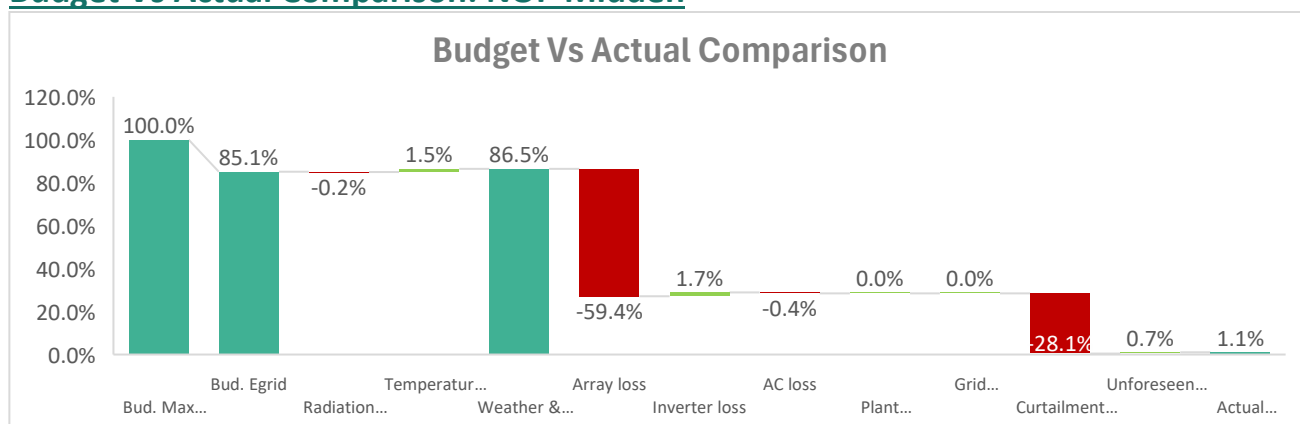

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(M Wh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(M Wh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	2,367	2,015	-4	24	2,047	-1,405	41	-9	-	-665	17	26
	100.0%	85.1%	-0.2%	1.5%	86.5%	-59.4%	1.7%	-0.4%	0.0%	-28.1%	0.7%	1.1%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Grid & Curtailment losses are seen accounting for most of the technical reduction. Inverter and Temperature factor are contributing more than their budgeted numbers. Overall, 1.1% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: NOP Midden

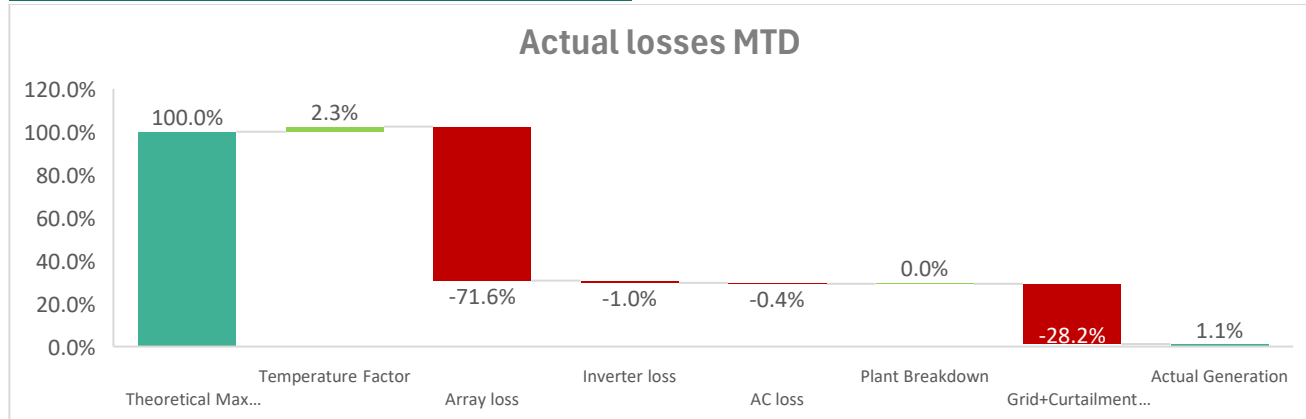

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2362	55	-1692	-25	-9	0	-665	26
	100.0%	2.3%	-71.6%	-1.0%	-0.4%	0.0%	-28.2%	1.1%

From the Theoretical Max generation baseline an Array, Inverter, Grid & Curtailment losses are seen accounting for most of the technical reduction. Overall, 1.1% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: NOP Midden

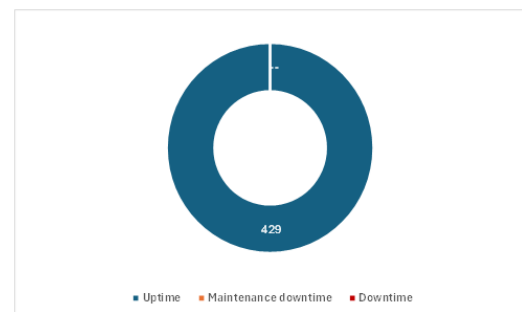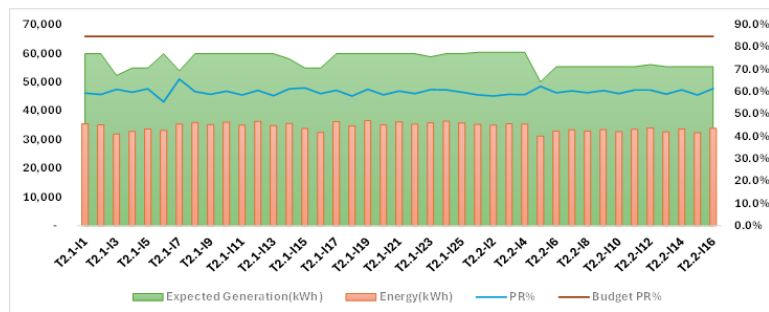

Top 5 Inverters

Inverter Name	PR%	Yield
T2.1-17	65.6%	97.4
T2.1-114	61.2%	90.9
T2.1-115	61.6%	91.5
T2.2-15	62.4%	92.6
T2.2-116	61.3%	91.0

Bottom 5 Inverters

Inverter Name	PR%	Yield
T2.1-16	55.4%	82.2

Downtime Details

- Maintenance: NA
- Downtime: NA

String Performance Report: NOP Midden


Total Strings:	984
Normal Strings:	880
Underperforming Strings Z-Score<-1:	66
Faulty Strings Z-Score<-2:	4
Severe Strings Z-Score<-3:	34

Underperforming Strings	Deviation%	Severe Strings	Deviation%
INV-1.9_DC7_1	-9.2%	INV-1.10_DC5_2	-100.0%
INV-1.9_DC7_2	-9.8%	INV-1.11_DC10_2	-100.0%
INV-1.9_DC9_2	-8.1%	INV-1.11_DC5_2	-100.0%
INV-1.13_DC1_2	-8.1%	INV-1.12_DC10_2	-100.0%
INV-1.13_DC10_2	-8.1%	INV-1.12_DC5_2	-100.0%

7. Performance Analysis Report: NOP Noord

AC Capacity (MW): 16.3 MW DC Capacity (MWp): 25.2 MWp Location: NL


MTD Report: NOP Noord

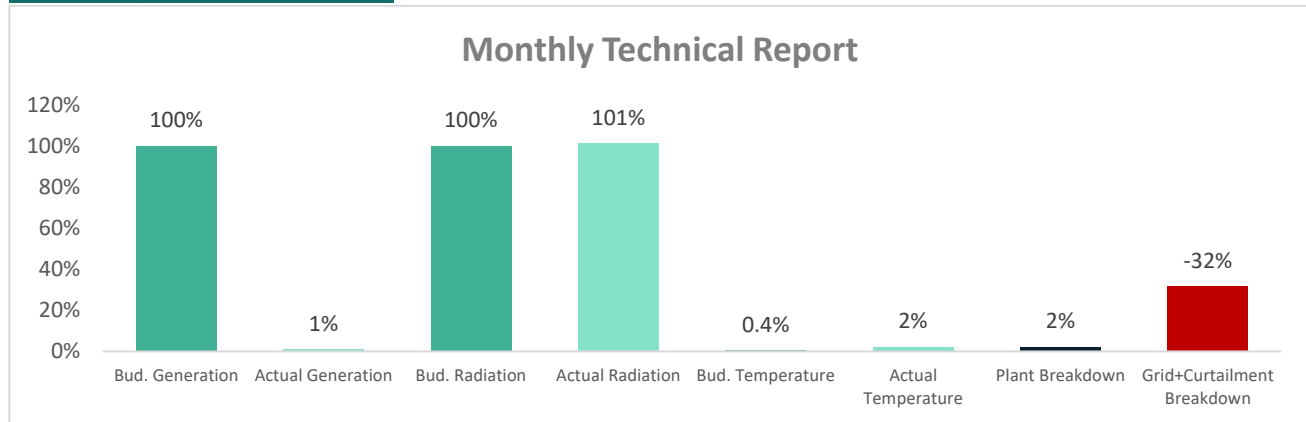

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)
Apr-26	3,260	35	149	151	16	90	-75	-1,032
	100.0%	1.1%	100.0%	101.3%	0.4%	2.3%	2.3%	31.7%

From the above graph it is clearly visible that the Actual Generation achieved 1.1% of Budgeted Generation, Actual Radiation is 101.3% of Budgeted Radiation.


Budget Vs Actual Comparison: NOP Noord

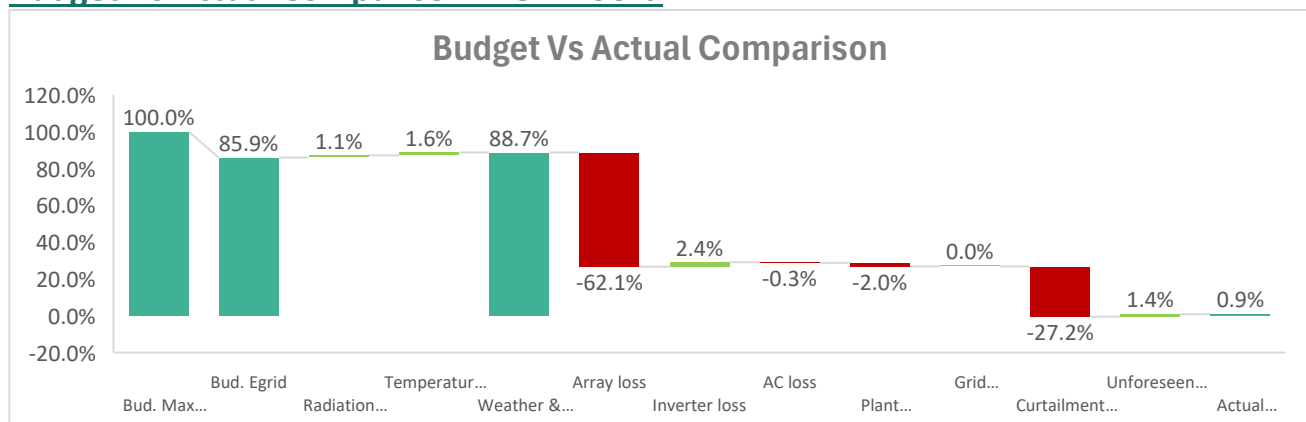

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(M Wh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(M Wh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	3,794	3,260	43	45	3,365	-2,356	90	-10	-74.6	-1,032	53	35
	100.0%	85.9%	1.1%	1.6%	88.7%	-62.1%	2.4%	-0.3%	-2.0%	-27.2%	1.4%	0.9%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, Plant and Grid & Curtailment losses are seen accounting for most of the technical reduction. Radiation and Temperature are contributing more than their budgeted numbers. Overall, 0.9% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: NOP Noord

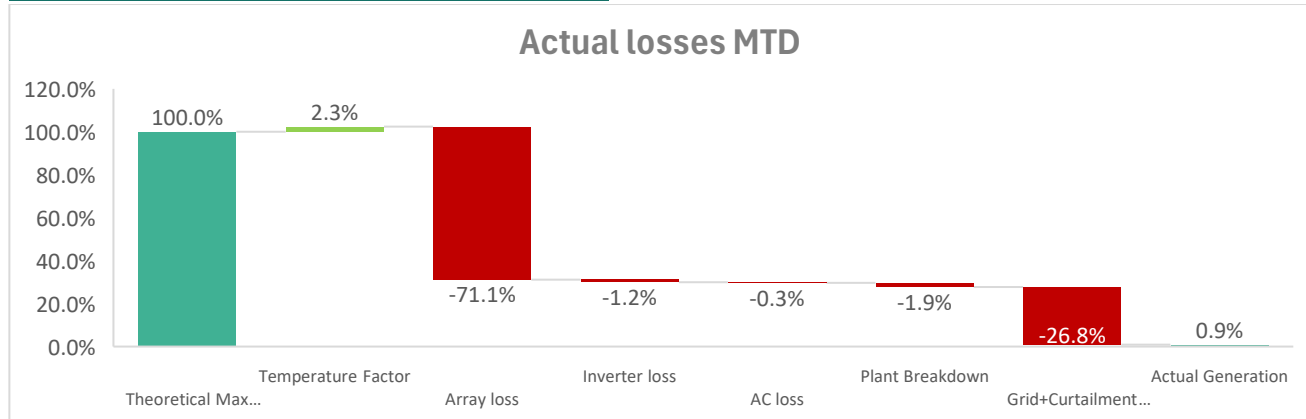

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	3845	90	-2735	-47	-10	-75	-1032	35
	100.0%	2.3%	-71.1%	-1.2%	-0.3%	-1.9%	-26.8%	0.9%

From the Theoretical Max generation baseline an Array, Inverter and Grid & Curtailment losses are seen accounting for most of the technical reduction. Overall, 0.9% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: NOP Noord

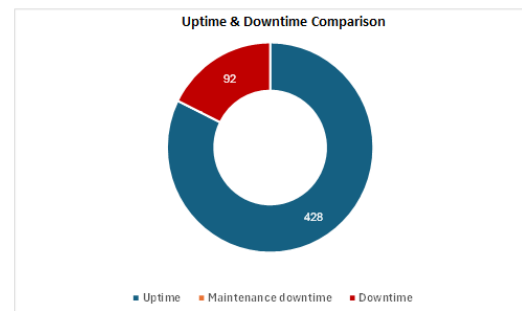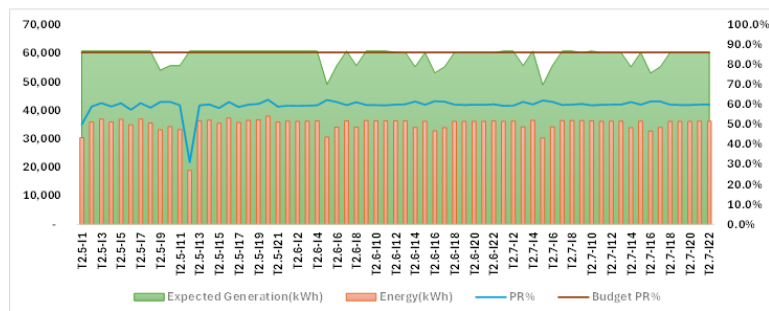

Top 5 Inverters

InverterName	PR%	Yield
T2.5-I20	62.4%	94.1
T2.6-I5	62.4%	94.1
T2.7-I5	62.1%	93.6
T2.7-I16	61.6%	92.9
T2.7-I17	61.6%	92.9

Bottom 5 Inverters

Inverter Name	PR%	Yield
T2.5-I1	50.1%	75.5
T2.5-I12	31.2%	47.0

Downtime Details

1. Maintenance: NA
2. Downtime: 25 days, Impact: 74.6MWh

String Performance Report: NOP Noord


Total Strings: 1560
Normal Strings: 1382
Underperforming Strings Z-Score<-1: 140
Faulty Strings Z-Score<-2: 12
Severe Strings Z-Score<-3: 26

Underperforming Strings	Deviation%	Severe Strings	Deviation%
INV-T2.5.3_DC7_1	-10.6%	INV-T2.6.5_DC6_2	-100.0%
INV-T2.5.3_DC7_2	-11.3%	INV-T2.6.5_DC12_2	-100.0%
INV-T2.5.3_DC8_2	-12.7%	INV-T2.6.6_DC6_2	-100.0%
INV-T2.5.3_DC9_2	-11.1%	INV-T2.6.6_DC12_2	-100.0%
INV-T2.5.4_DC7_2	-10.9%	INV-T2.6.8_DC6_2	-100.0%

8. Performance Analysis Report: NOP Plot4

AC Capacity (MW): 9.3 MW DC Capacity (MWp): 14.4 MWp Location: NL


MTD Report: NOP Plot4

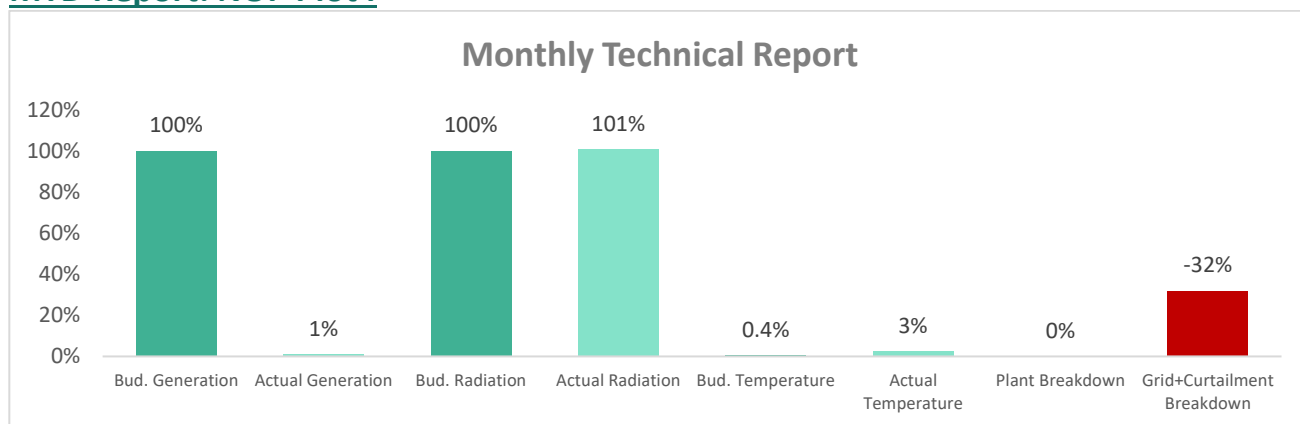

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	1,860	20	149	150	10	56	-	-594
	100.0%	1.1%	100.0%	100.7%	0.4%	2.6%	0.0%	32.0%

From the above graph it is clearly visible that the Actual Generation achieved 1.1% of Budgeted Generation, Actual Radiation is 100.7% of Budgeted Radiation.


Budget Vs Actual Comparison: NOP Plot4

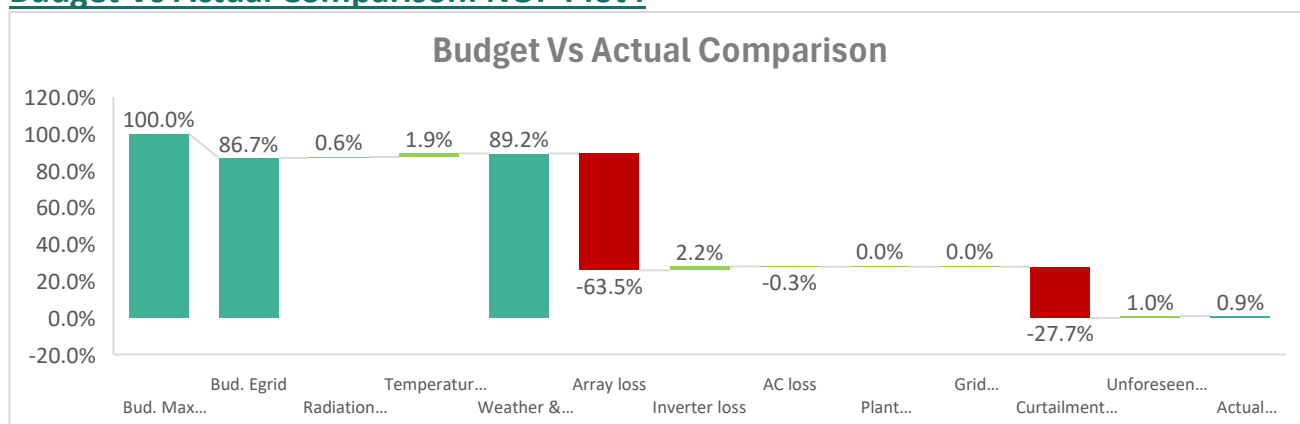

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	2,146	1,860	14	30	1,914	-1,363	47	-6	-	-594	22	20
	100.0%	86.7%	0.6%	1.9%	89.2%	-63.5%	2.2%	-0.3%	0.0%	-27.7%	1.0%	0.9%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Grid & Curtailment losses are seen accounting for most of the technical reduction. Radiation and Temperature are contributing more than their budgeted numbers. Overall, 0.9% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: NOP Plot4

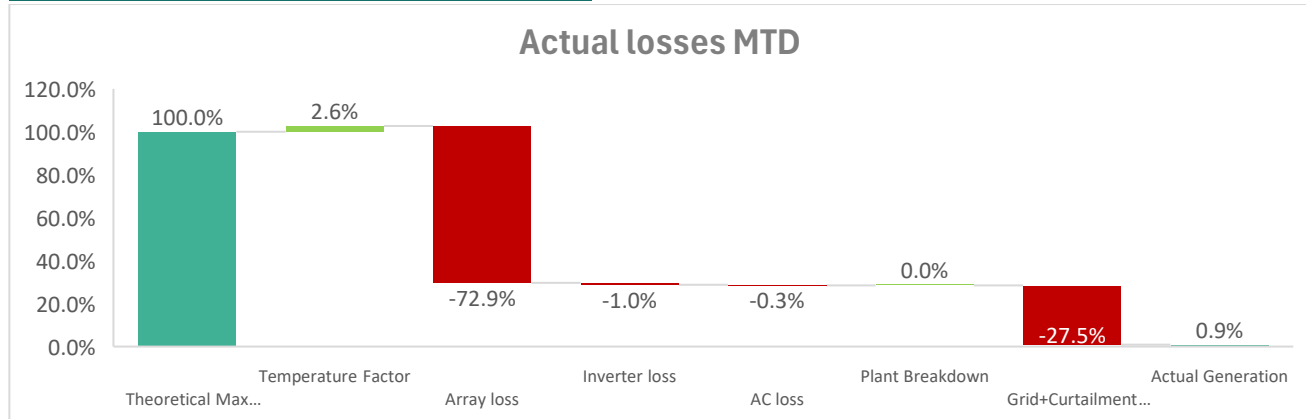

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2162	56	-1577	-21	-6	0	-594	20
	100.0%	2.6%	-72.9%	-1.0%	-0.3%	0.0%	-27.5%	0.9%

From the Theoretical Max generation baseline an Array, Inverter and Grid & Curtailment losses are seen accounting for most of the technical reduction. Overall, 0.9% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: NOP Plot4

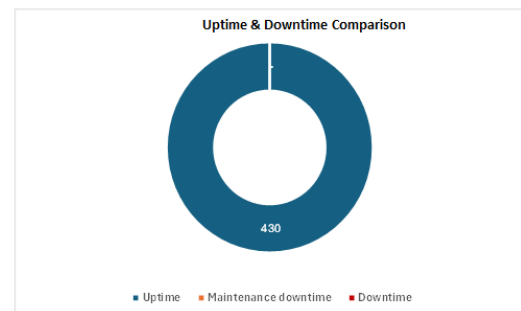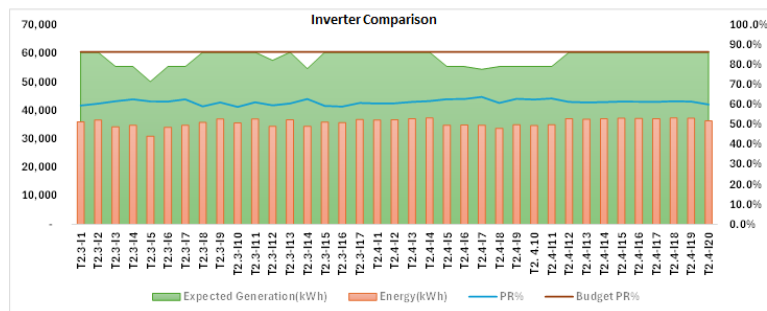

Top 5 Inverters

Inverter Name	PR%	Yield
T2.3-I7	62.7%	94.0
T2.3-I14	62.8%	94.1
T2.4-I7	63.9%	95.8
T2.4-I8	60.8%	91.2
T2.4-I11	63.1%	94.6

Bottom 5 Inverters

Inverter Name	PR%	Yield
T2.3-I8	59.2%	88.7
T2.3-I10	58.9%	88.3
T2.3-I15	59.4%	89.0
T2.3-I16	59.0%	88.5
T2.4-I20	60.0%	90.0

Downtime Details

- Maintenance: NA
- Downtime: NA

String Performance Report: NOP Plot4


Total Strings:	888
Normal Strings:	825
Underperforming Strings Z-Score<-1:	36
Faulty Strings Z-Score<-2:	0
Severe Strings Z-Score<-3:	27

Underperforming Strings	Deviation%	Severe Strings	Deviation%
INV-T2.3.2_DC8_2	-7.4%	INV-T2.3.3_DC12_2	-100.0%
INV-T2.3.2_DC9_2	-7.6%	INV-T2.3.4_DC6_2	-100.0%
INV-T2.3.2_DC12_2	-7.5%	INV-T2.3.4_DC12_2	-100.0%
INV-T2.3.9_DC8_2	-7.6%	INV-T2.3.5_DC6_2	-100.0%
INV-T2.3.9_DC10_2	-7.7%	INV-T2.3.5_DC12_2	-100.0%

9. Performance Analysis Report: NOP Zuid

AC Capacity (MW): 26.8 MW DC Capacity (MWp): 40 MWp Location: NL


MTD Report: NOP Zuid

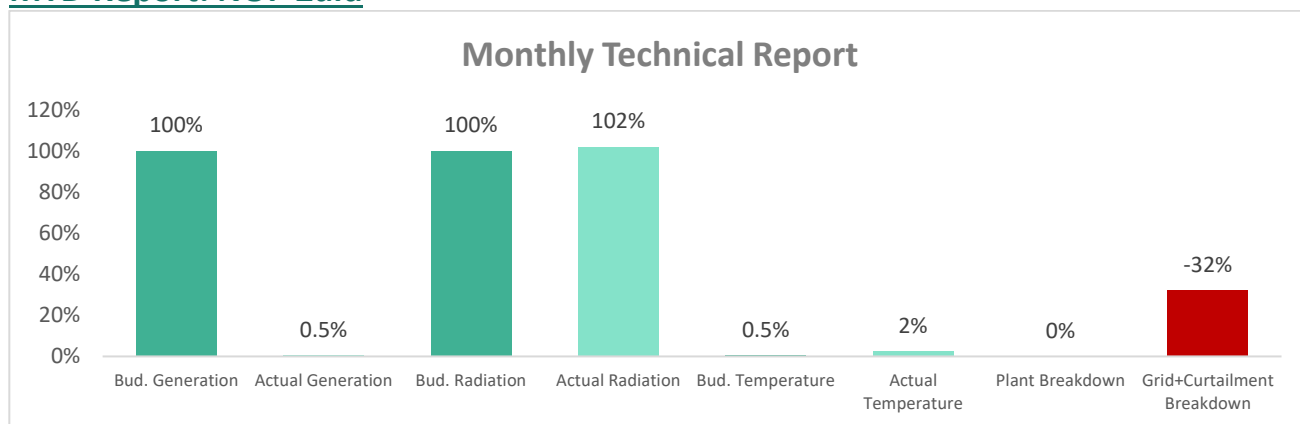

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)
Apr-26	5,182	25	149	152	27	145	-	-1,661
	100.0%	0.5%	100.0%	101.9%	0.5%	2.4%	0.0%	32.1%

From the above graph it is clearly visible that the Actual Generation achieved 0.5% of Budgeted Generation, Actual Radiation is 101.9% of Budgeted Radiation.


Budget Vs Actual Comparison: NOP Zuid

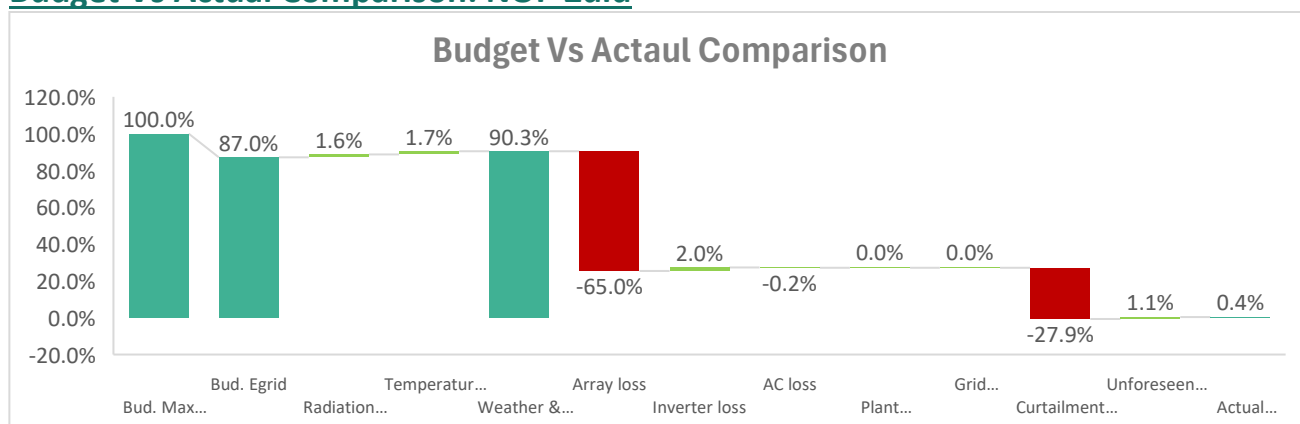

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	5,956	5,182	98	73	5,380	-3,872	119	-10	-	-1,661	68	25
	100.0%	87.0%	1.6%	1.7%	90.3%	-65.0%	2.0%	-0.2%	0.0%	-27.9%	1.1%	0.4%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Grid & Curtailment losses are seen accounting for most of the technical reduction. Radiation and Temperature are contributing more than their budgeted numbers. Overall, 0.4% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: NOP Zuid

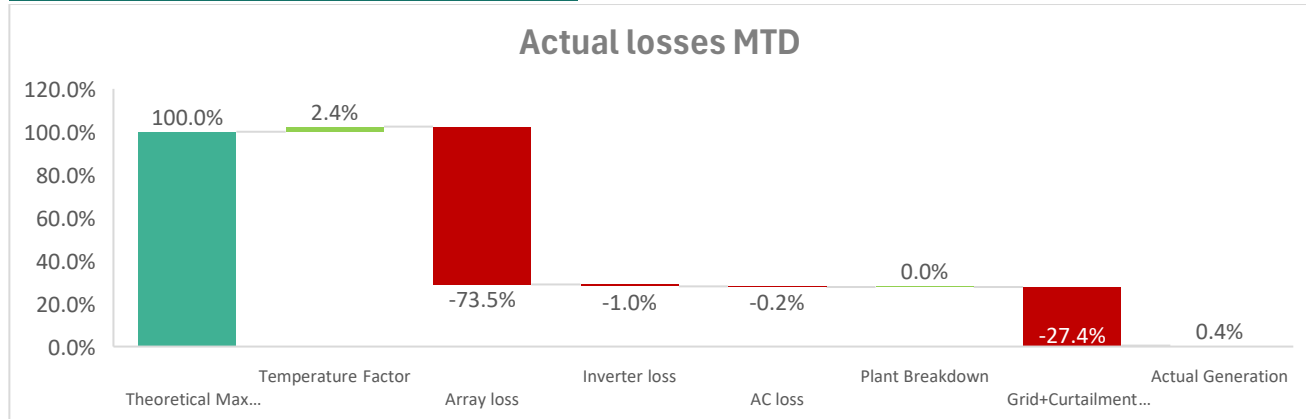

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	6069	145	-4460	-59	-10	0	-1661	25
	100.0%	2.4%	-73.5%	-1.0%	-0.2%	0.0%	-27.4%	0.4%

From the Theoretical Max generation baseline an Array, Inverter and Grid & curtailment losses are seen accounting for most of the technical reduction. Overall, 0.4% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: NOP Zuid

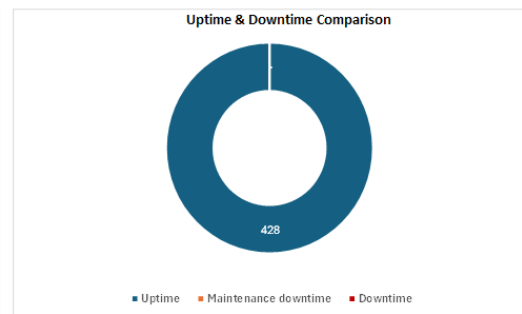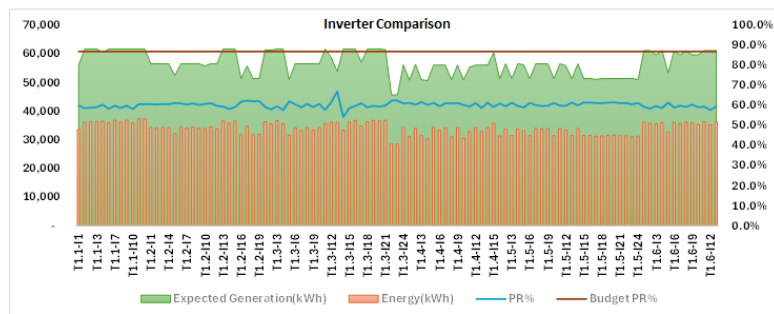

Top 5 Inverters

Inverter Name	PR%	Yield
T1.2-I19	62.2%	94.2
T1.3-I5	62.0%	94.0
T1.3-I13	66.9%	101.5
T1.3-I22	62.4%	94.5
T1.3-I23	62.3%	94.5

Bottom 5 Inverters

Inverter Name	PR%	Yield
T1.3-I14	54.2%	82.2

Downtime Details

- Maintenance: NA
- Downtime: NA

String Performance Report: NOP Zuid


Total Strings:	2568
Normal Strings:	2282
Underperforming Strings Z-Score<-1:	103
Faulty Strings Z-Score<-2:	110
Severe Strings Z-Score<-3:	73

Underperforming Strings	Deviation%	Severe Strings	Deviation%
INV-T1.3.3_DC9_2	-8.1%	INV-T1.1.1_DC5_2	-100.0%
INV-T1.3.3_DC11_2	-7.6%	INV-T1.1.1_DC11_2	-100.0%
INV-T1.3.3_DC12_2	-7.8%	INV-T1.2.1_DC6_2	-100.0%
INV-T1.3.4_DC7_1	-9.1%	INV-T1.2.1_DC12_2	-100.0%
INV-T1.3.4_DC7_2	-9.2%	INV-T1.2.2_DC6_2	-100.0%

10. Performance Analysis Report: Snelle loop

AC Capacity (MW): 26.8 MW DC Capacity (MWp): 20 MWp Location: NL


MTD Report: Snelle loop

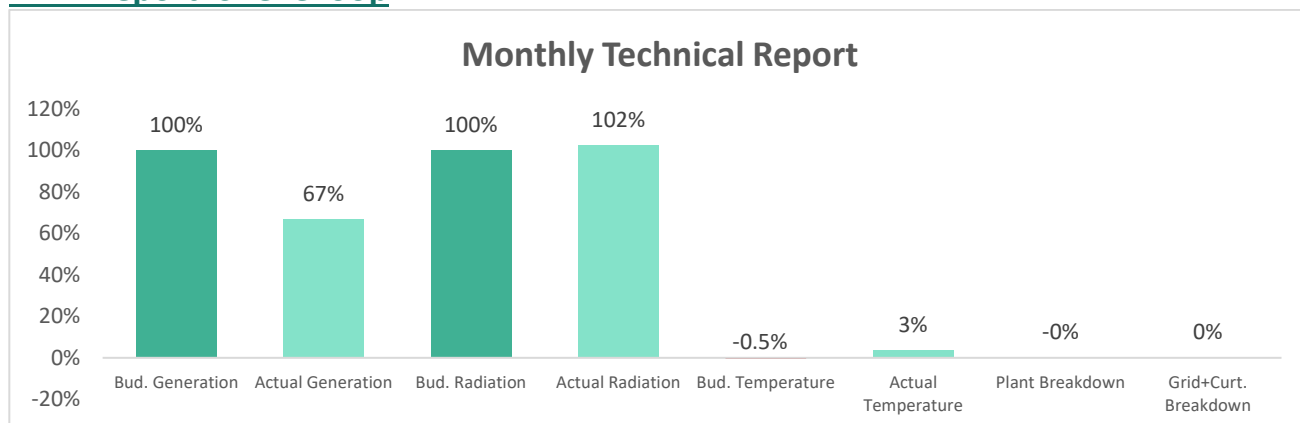

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MW h)	Actual Temperature Factor(MW h)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	3,653	2,444	159	162	-20	149	-15	-
	100.0%	66.9%	100.0%	102.2%	-0.5%	3.4%	0.4%	0.0%

From the above graph it is clearly visible that the Actual Generation achieved 66.9% of Budgeted Generation, Actual Radiation is 102.2% of Budgeted Radiation.


Budget Vs Actual Comparison: Snelle loop

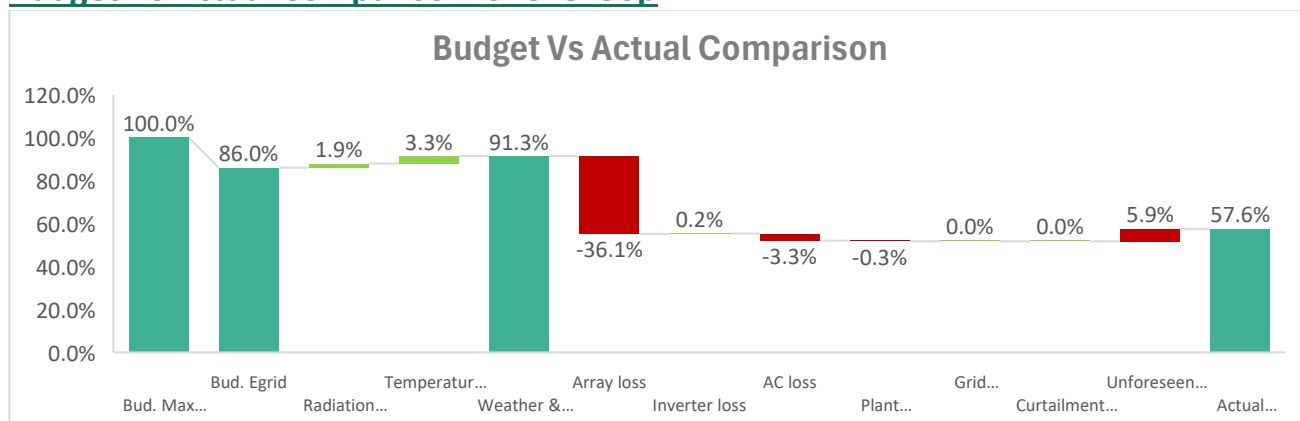

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid (MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid (MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	4,247	3,653	81	161	3,875	-1,535	7	-86	-14.6	-	250	2,444
	100.0%	86.0%	1.9%	3.3%	91.3%	-36.1%	0.2%	-3.3%	-0.3%	0.0%	5.9%	57.6%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array and Plant losses are seen accounting for most of the technical reduction. Radiation and Temperature are contributing more than their budgeted numbers. Overall, 57.6% of actual generation is achieved of budgeted max theoretical numbers.

MTD Actual Losses Report: Snelle loop

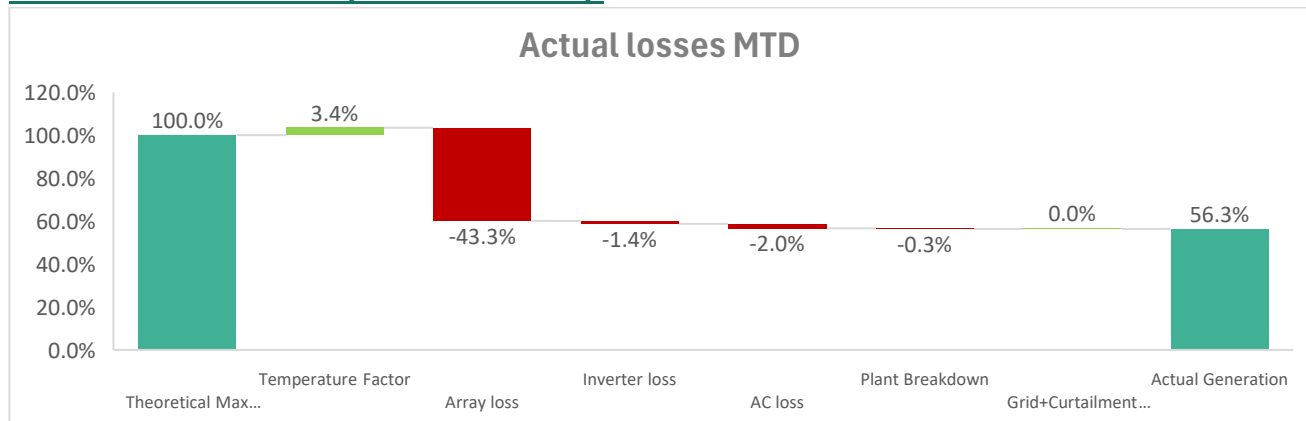


Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailed Breakdown (MWh)	Actual Generation (MWh)
Apr-26	4342	149	-1881	-63	-88	-15	0	2444
	100.0%	3.4%	-43.3%	-1.4%	-2.0%	-0.3%	0.0%	56.3%

From the Theoretical Max generation baseline an Array, Inverter losses are seen accounting for most of the technical reduction. Overall, 56.3% of actual generation is achieved of theoretical max numbers.

11. Performance Analysis Report: Gorgast Bahn

AC Capacity (MW): 14 MW DC Capacity (MWp): 15 MWp Location: DE


MTD Report: Gorgast Bahn

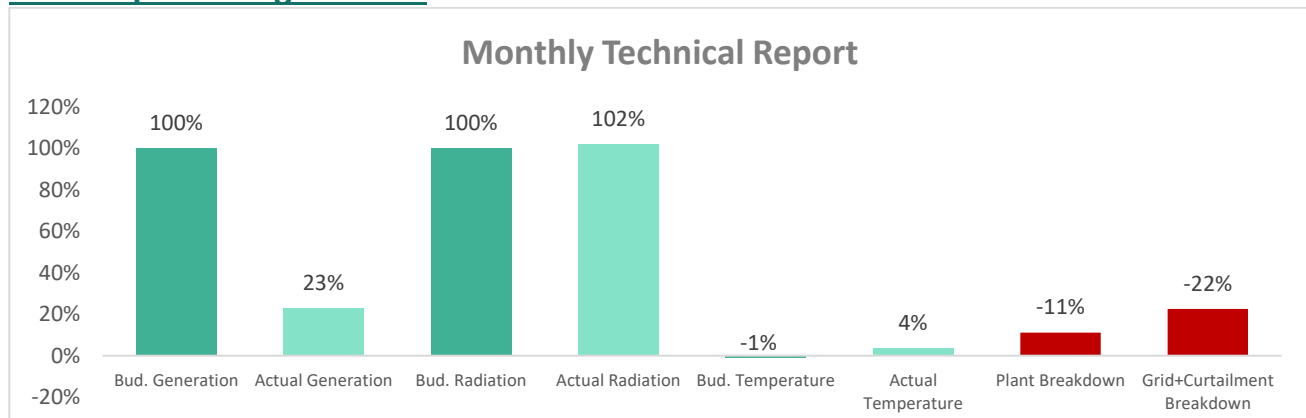

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	2,006	457	154	157	-19	85	-222	-451
	100.0%	22.8%	100.0%	102.0%	-0.8%	3.6%	11.1%	22.5%

From the above graph it is clearly visible that the Actual Generation achieved 22.8% of Budgeted Generation, Actual Radiation is 102.0% of Budgeted Radiation.


Budget Vs Actual Comparison: Gorgast Bahn

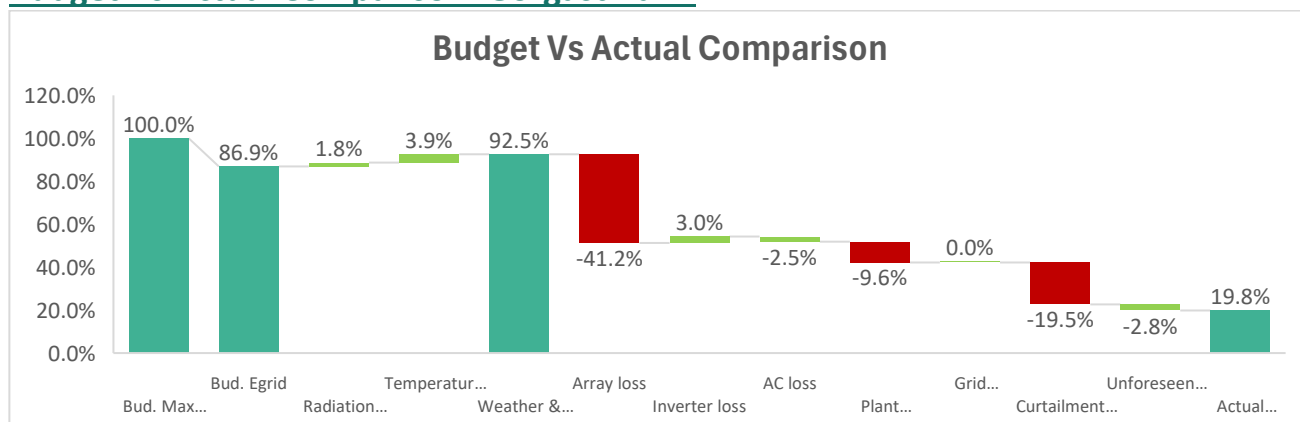

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	2,309	2,006	41	108	2,135	-951	69	-46	-221.6	-451	-66	457
	100.0%	86.9%	1.8%	3.9%	92.5%	-41.2%	3.0%	-2.5%	-9.6%	-19.5%	-2.8%	19.8%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, AC, Plant and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Radiation and Temperature are contributing more than their budgeted numbers. Overall, 19.8% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Gorgast Bahn

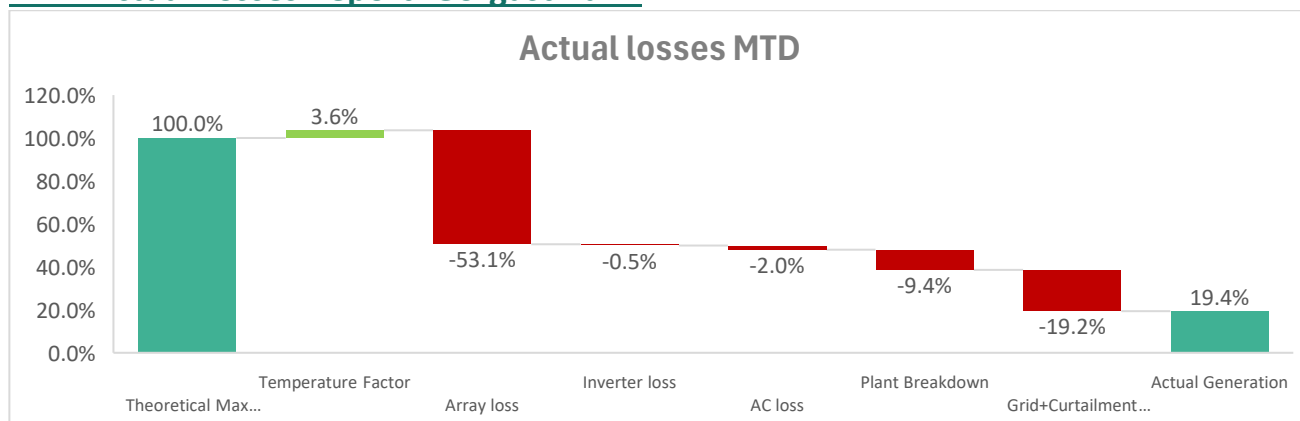

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2355	85	-1250	-13	-47	-222	-451	457
	100.0%	3.6%	-53.1%	-0.5%	-2.0%	-9.4%	-19.2%	19.4%

From the Theoretical Max generation baseline an Array, AC and Plant and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Overall, 19.4% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Gorgast Bahn

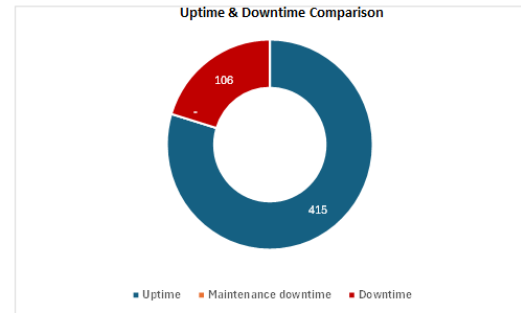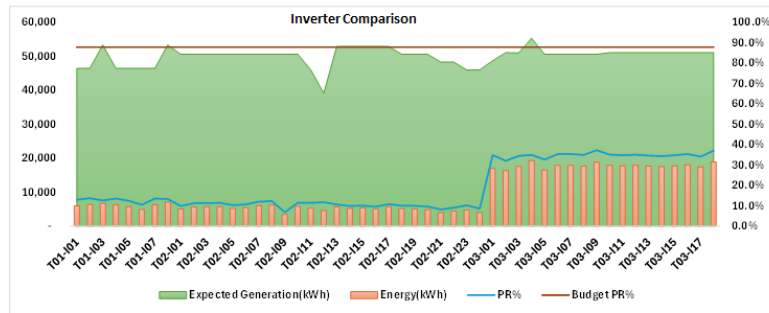

Top 5 Inverters

Inverter Name	PR%	Yield
T03-I06	35.3%	58.8
T03-I07	35.3%	58.8
T03-I09	37.2%	61.9
T03-I10	35.1%	58.4
T03-I18	37.0%	61.6

Bottom 5 Inverters

Inverter Name	PR%	Yield
T02-I09	6.8%	11.3
T02-I16	9.5%	15.9
T02-I21	8.2%	13.6
T02-I22	9.0%	15.0
T02-I24	8.6%	14.2

Downtime Details

1. Maintenance: NA
2. Downtime: 20 days, Impact: 221.6MWh

String Performance Report: Gorgast Bahn


Total Strings: 1086
Normal Strings: 955
Underperforming Strings Z-Score<-1: 128
Faulty Strings Z-Score<-2: 3
Severe Strings Z-Score<-3: 0

Underperforming Strings	Deviation%	Faulty Strings	Deviation%
INV19.DC20	-19.7%	INV06.DC14	-52.9%
INV21.DC15	-17.7%	INV06.DC16	-54.0%
INV22.DC16	-19.0%	INV06.DC4	-54.4%
		INV06.DC6	-50.4%
		INV06.DC8	-55.8%

12. Performance Analysis Report: Gorgast Gewachshaus

AC Capacity (MW): 10.56 MW DC Capacity (MWp): 15 MWp Location: DE


MTD Report: Gorgast Gewachshaus

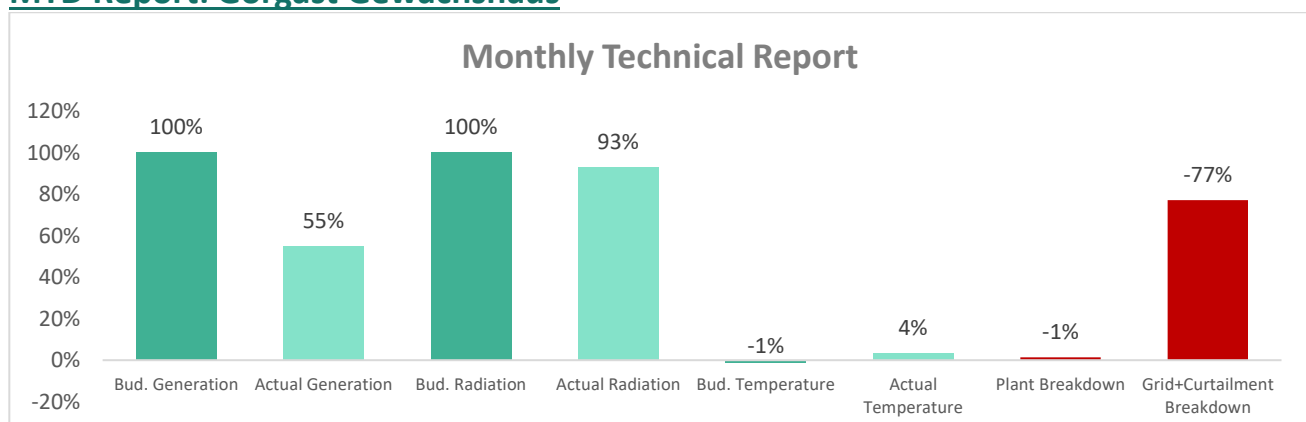

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	1,683	923	147	136	-25	69	-23	-1,297
	100.0%	54.8%	100.0%	93.1%	-1.2%	3.5%	1.4%	77.1%

From the above graph it is clearly visible that the Actual Generation achieved 54.8% of Budgeted Generation, Actual Radiation is 93.1% of Budgeted Radiation.


Budget Vs Actual Comparison: Gorgast Gewachshaus

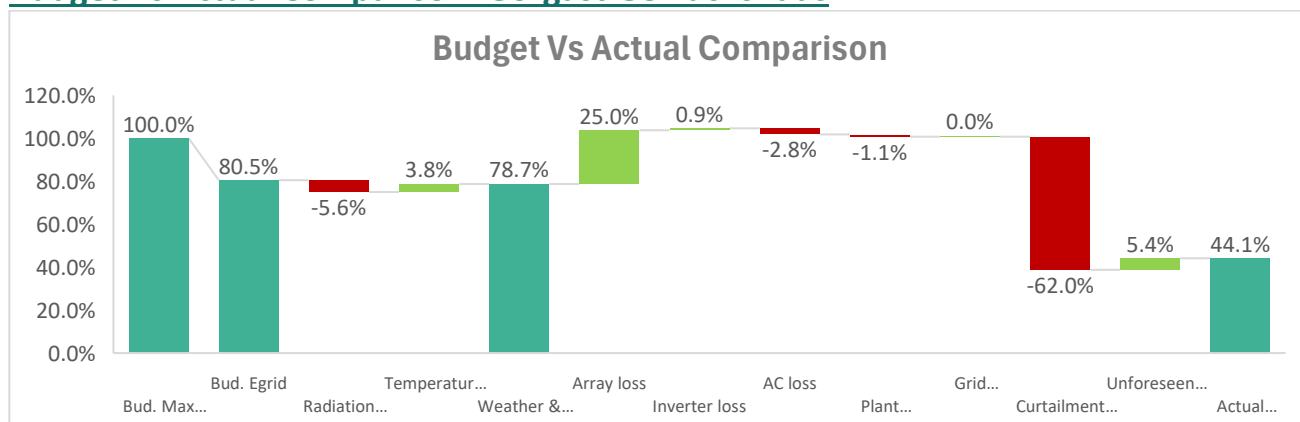

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	2,092	1,683	-117	105	1,646	524	18	-42	-22.9	-1,297	112	923
	100.0%	80.5%	-5.6%	3.8%	78.7%	25.0%	0.9%	-2.8%	-1.1%	-62.0%	5.4%	44.1%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Radiation, AC, Plant and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Temperature and Array losses are contributing more than their budgeted numbers. Overall, 44.1% of actual generation is achieved of budgeted max theoretical numbers.


MTD Actual Losses Report: Gorgast Gewachshaus

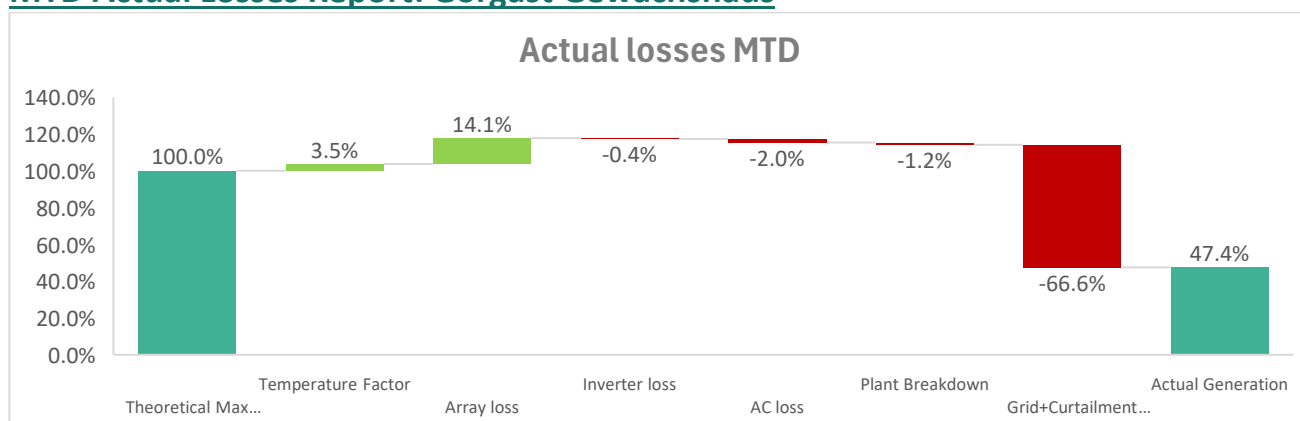

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	1947	69	274	-9	-39	-23	-1297	923
	100.0%	3.5%	14.1%	-0.4%	-2.0%	-1.2%	-66.6%	47.4%

From the Theoretical Max generation baseline an AC, Plant and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Overall, 47.4% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Gorgast Gewachshaus

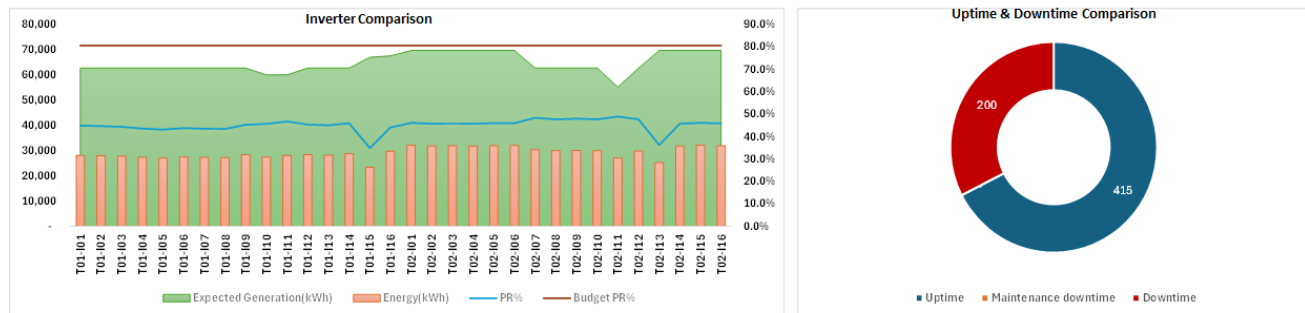

Top 5 Inverters

InverterName	PR%	Yield
T02-107	48.3%	70.2
T02-108	47.7%	69.2
T02-109	47.9%	69.5
T02-110	47.6%	69.1
T02-111	48.9%	70.9

Bottom 5 Inverters

InverterName	PR%	Yield
T01-115	34.8%	50.5
T02-113	36.2%	52.5

Downtime Details

1. Maintenance: NA
2. Downtime: 16 days, Impact: 22.8MWh

String Performance Report: Gorgast Gewachshaus


Total Strings: 894
Normal Strings: 603
Underperforming Strings Z-Score<-1: 0
Faulty Strings Z-Score<-2: 0
Severe Strings Z-Score<-3: 291

Severe Strings	Deviation%
INV01.DC25	-100%
INV01.DC27	-100%
INV01.DC29	-100%
INV01.DC31	-100%
INV02.DC21	-100%

13. Performance Analysis Report: Gorgast Manschnow

AC Capacity (MW): 11.52 MW DC Capacity (MWp): 15.65 MWp Location: DE


MTD Report: Gorgast Manschnow

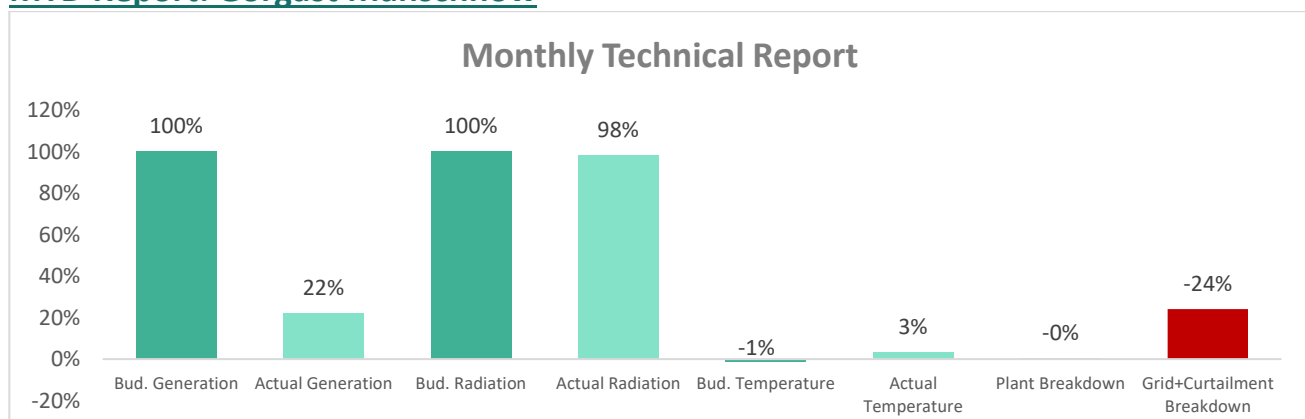

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	1,827	406	146	143	-27	77	-3	-441
	100.0%	22.2%	100.0%	98.1%	-1.2%	3.4%	0.2%	24.1%

From the above graph it is clearly visible that the Actual Generation achieved 22.2% of Budgeted Generation, Actual Radiation is 98.1% of Budgeted Radiation.


Budget Vs Actual Comparison: Gorgast Manschnow

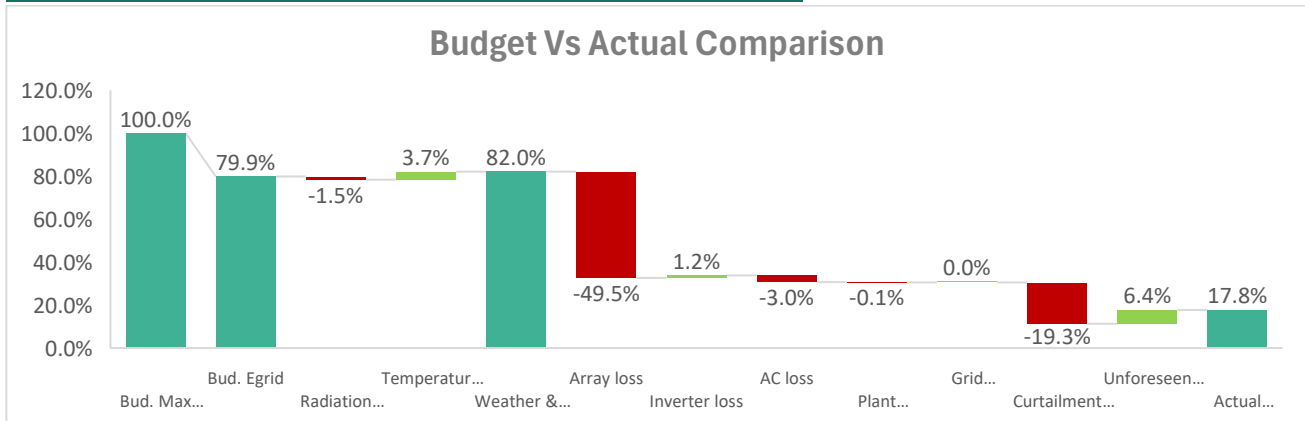

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	2,288	1,827	-34	111	1,877	-1,132	27	-46	-3.4	-441	147	406
	100.0%	79.9%	-1.5%	3.7%	82.0%	-49.5%	1.2%	-3.0%	-0.1%	-19.3%	6.4%	17.8%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, AC and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reductions. Temperature and Inverter are contributing more than their budgeted numbers. Overall, 17.8% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Gorgast Manschnow

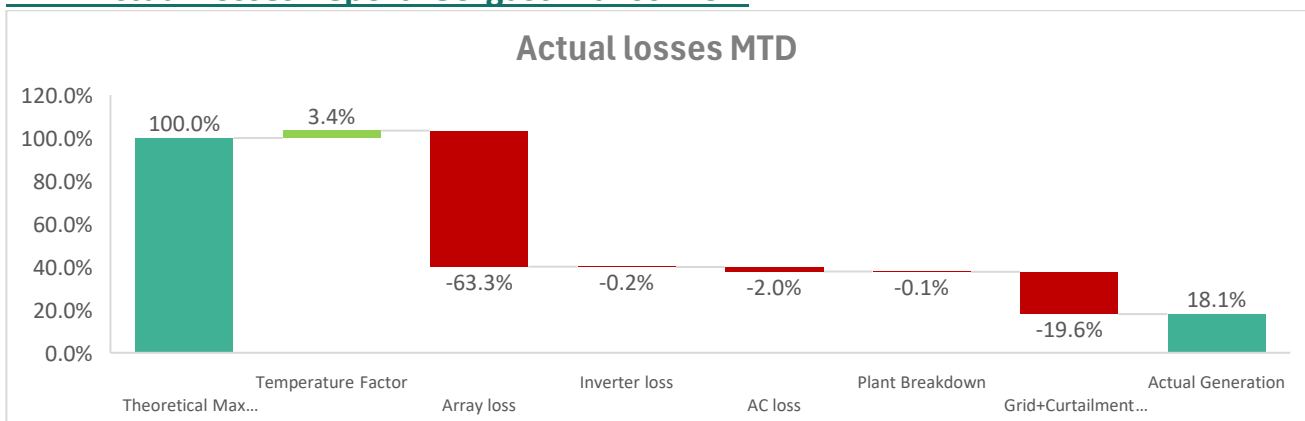

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	2245	77	-1422	-4	-45	-3	-441	406
	100.0%	3.4%	-63.3%	-0.2%	-2.0%	-0.1%	-19.6%	18.1%

From the Theoretical Max generation baseline an Array, AC and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Overall, 18.1% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Gorgast Manschnow

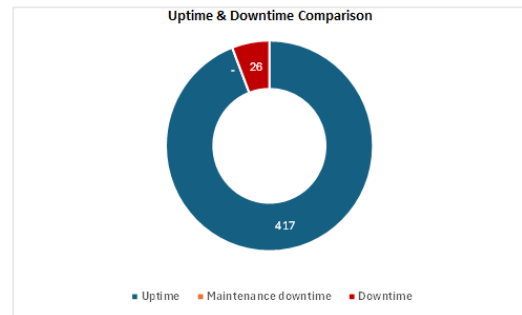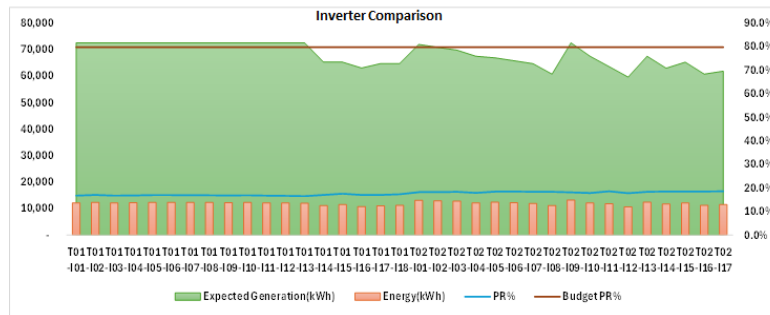

Top 5 Inverters

Inverter Name	PR%	Yield
T02 -I13	18.4%	28.0
T02 -I14	18.5%	28.2
T02 -I15	18.5%	28.2
T02 -I16	18.5%	28.2
T02 -I17	18.6%	28.3

Bottom 5 Inverters

Inverter Name	PR%	Yield
T01 -I01	16.7%	25.5
T01 -I03	16.7%	25.5
T01 -I11	16.8%	25.6
T01 -I12	16.6%	25.4
T01 -I13	16.6%	25.2

Downtime Details

1. Maintenance: NA
2. Downtime: 10 days, Impact: 3.3MWh

String Performance Report: Gorgast Manschnow


Total Strings: 1004
Normal Strings: 689
Underperforming Strings Z-Score<-1: 0
Faulty Strings Z-Score<-2: 0
Severe Strings Z-Score<-3: 315

Severe Strings	Deviation%
INV01.DC21	-100%
INV01.DC22	-100%
INV01.DC23	-100%
INV01.DC24	-100%
INV01.DC25	-100%

14. Performance Analysis Report: Northwold

AC Capacity (MW): 10 MW DC Capacity (MWp): 10 MWp Location: UK


MTD Report: Northwold

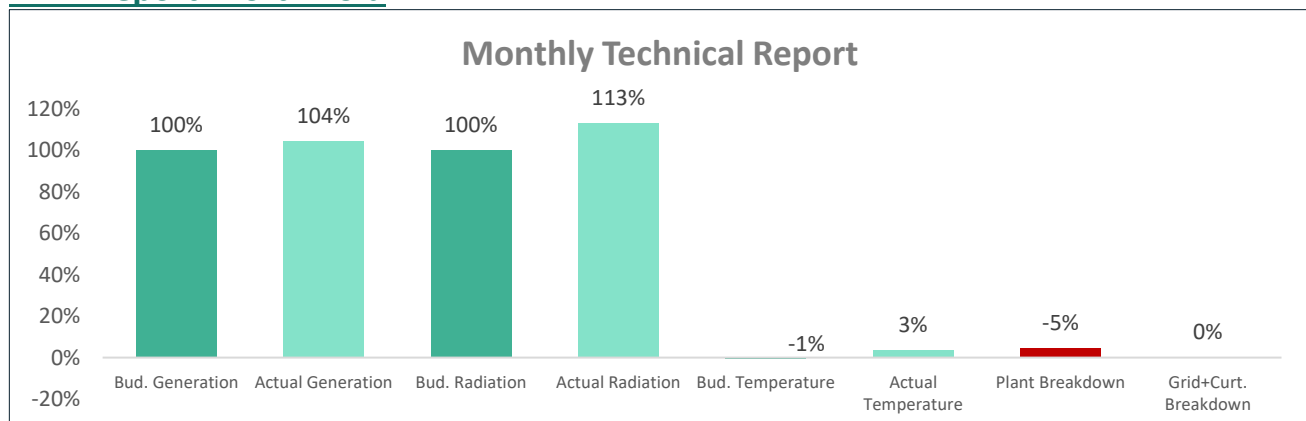

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MW h)	Actual Temperature Factor(MW h)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)
Apr-26	1,379	1,436	151	171	-8	59	-64	-
	100.0%	104.1%	100.0%	113.1%	-0.5%	3.5%	4.6%	0.0%

From the above graph it is clearly visible that the Actual Generation achieved 104.1% of Budgeted Generation, Actual Radiation is 113.1% of Budgeted Radiation.


Budget Vs Actual Comparison: Northwold

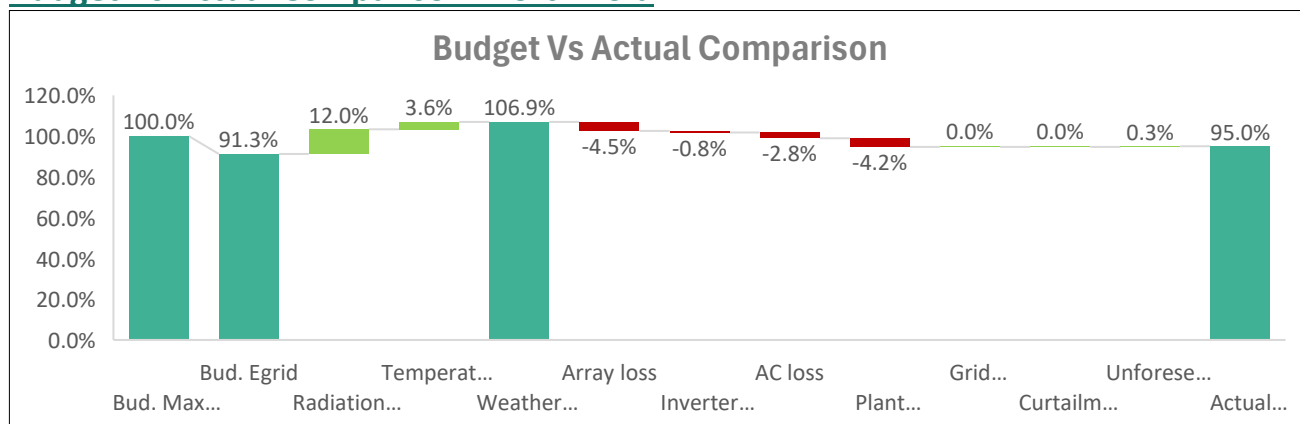

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(M Wh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(M Wh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	1,511	1,379	181	63	1,615	-68	-12	-31	-63.9	-	5	1,436
	100.0%	91.3%	12.0%	3.6%	106.9%	-4.5%	-0.8%	-2.8%	-4.2%	0.0%	0.3%	95.0%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array & AC losses are seen accounting for most of the technical reduction. Radiation and temperature losses are contributing more than their budgeted numbers. Overall, 95.0% of actual generation is achieved of budgeted max theoretical numbers.

MTD Actual Losses Report: Northwold


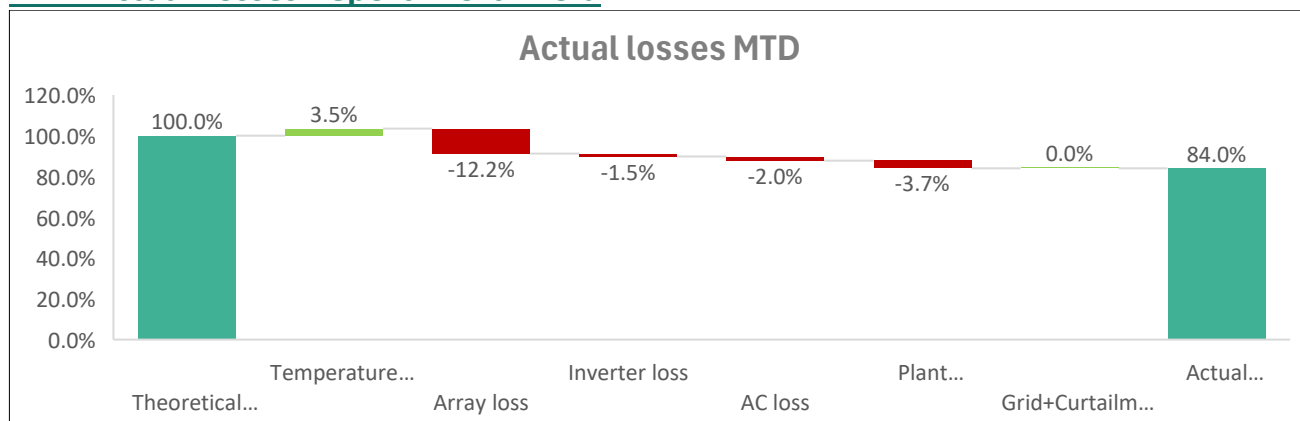


Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtaiment Breakdown (MWh)	Actual Generation (MWh)
Apr-26	1709	59	-209	-25	-35	-64	0	1436

	100.0%	3.5%	-12.2%	-1.5%	-2.0%	-3.7%	0.0%	84.0%
--	--------	------	--------	-------	-------	-------	------	-------

From the Theoretical Max generation baseline an Array, Inverter and AC losses are seen accounting for most of the technical reduction. Overall, 84.0% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Northwold

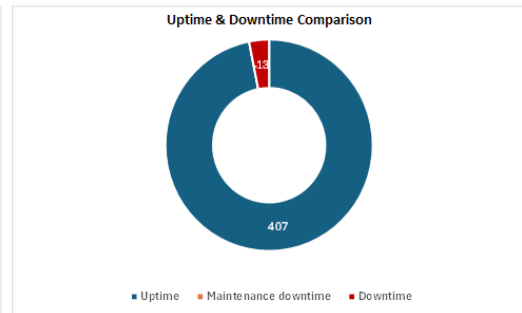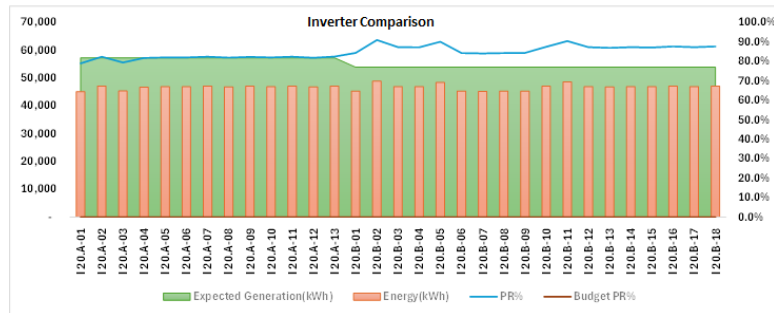

Top 5 Inverters

Inverter Name	PR%	Yield
I 20.B-02	90.8%	155.1
I 20.B-03	87.2%	149.0
I 20.B-05	89.9%	153.6
I 20.B-11	90.3%	154.3
I 20.B-12	87.2%	148.9

Bottom 5 Inverters

Inverter Name	PR%	Yield
I 20.A-01	78.8%	134.7
I 20.A-03	79.3%	135.5

Downtime Details

- Maintenance: NA
- Downtime: 2 days, Impact: 63.8

String Performance Report: Northwold


Total Strings: 585
Normal Strings: 465
Underperforming Strings Z-Score<-1: 111
Faulty Strings Z-Score<-2: 7
Severe Strings Z-Score<-3: 2

Underperforming Strings	Deviation%	Faulty Strings	Deviation%
String 20.A-02-03	-3.3%	String 20.B-05-18	-90.6%
String 20.A-03-09	-4.9%	String 20.B-16-01	-43.0%
String 20.A-03-12	-3.9%		
String 20.A-03-16	-3.2%		
String 20.A-04-04	-3.8%		

15. Performance Analysis Report: Edinburgh

AC Capacity (MW): 9.7 MW DC Capacity (MWp): 10 MWp Location: UK


MTD Report: Edinburgh

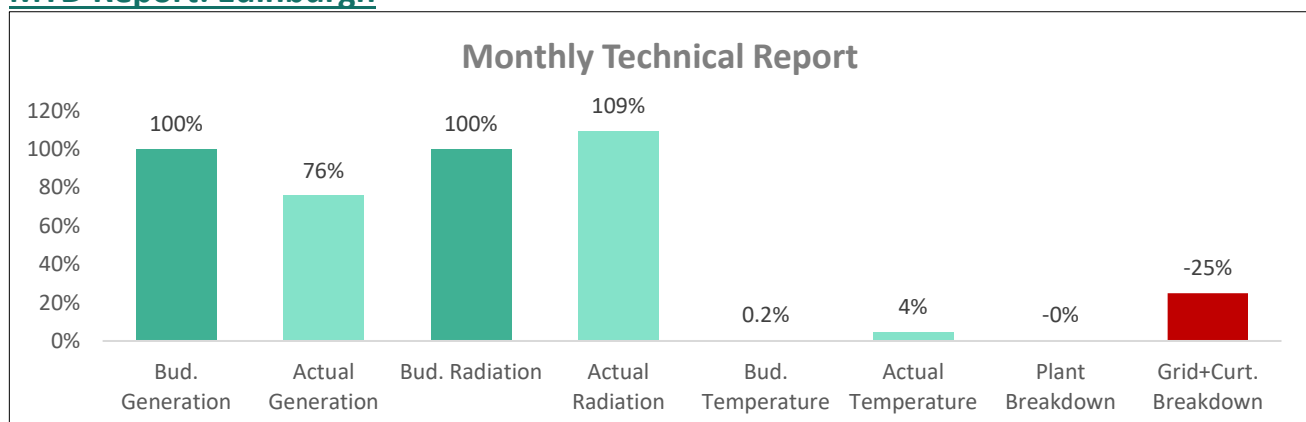

Date	Budgeted Generation (MWh)	Actual Generation (MWh)	Budgeted Radiation(k Wh/m^2)	Actual Radiation(k Wh/m^2)	Budgeted Temperature Factor(MWh)	Actual Temperature Factor(MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)
Apr-26	1,157	875	128	140	3	58	-4	-287
	100.0%	75.6%	100.0%	109.0%	0.2%	4.3%	0.4%	24.8%

From the above graph it is clearly visible that the Actual Generation achieved 75.6% of Budgeted Generation, Actual Radiation is 109.0% of Budgeted Radiation.


Budget Vs Actual Comparison: Edinburgh

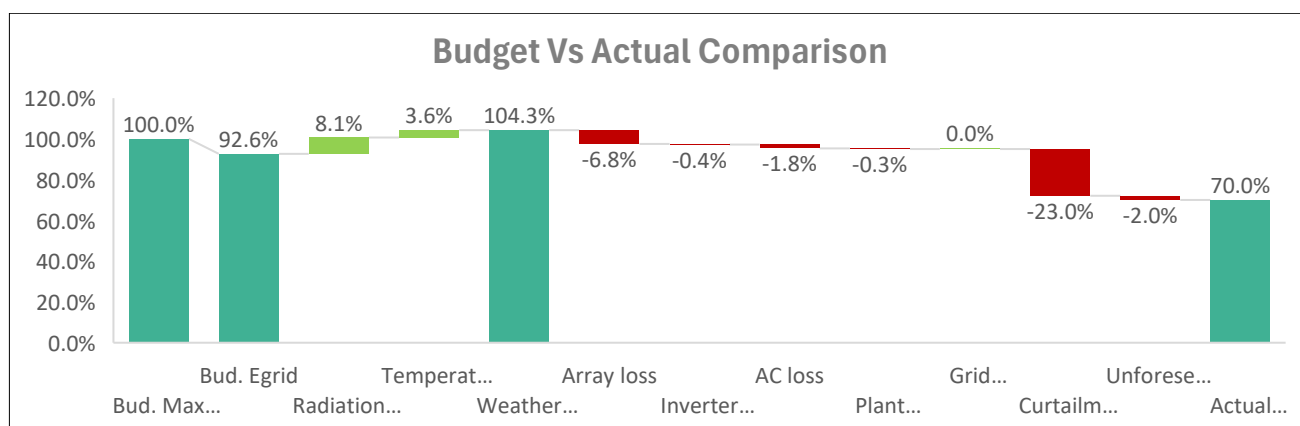

Month	Budgeted Max Theoretical Generation (MWh)	Budgeted Egrid(MWh)	Radiation Factor (MWh)	Temperature Factor (MWh)	Weather & Temperature Corrected Budgeted Egrid(MWh)	Array Loss (MWh)	Inverter Loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailment Breakdown (MWh)	Unforeseen Loss (MWh)	Actual Generation (MWh)
Apr-26	1,250	1,157	101	43	1,303	-85	-5	-19	-4.1	-287	-25	875
	100.0%	92.6%	8.1%	3.6%	104.3%	-6.8%	-0.4%	-1.8%	-0.3%	-23.0%	-2.0%	70.0%

From the Budgeted Max Theoretical generation baseline, this graph shows the delta between the budgeted max theoretical generation and actual generation. Array, AC and Grid & Curtailment Breakdown losses are seen accounting for most of the technical reduction. Radiation and temperature losses are contributing more than their budgeted numbers. Overall, 70.0% of actual generation is achieved of budgeted max theoretical numbers.



MTD Actual Losses Report: Edinburgh

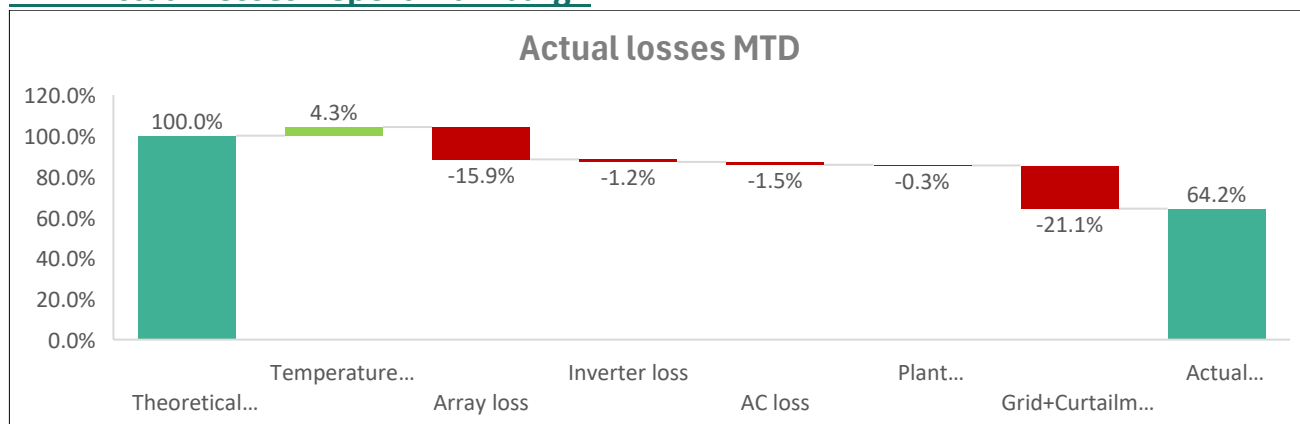

Month	Theoretical Max Generation (MWh)	Temperature Factor (MWh)	Array Loss (MWh)	Inverter loss (MWh)	AC Loss (MWh)	Plant Breakdown (MWh)	Grid+Curtailement Breakdown (MWh)	Actual Generation (MWh)
Apr-26	1362	58	-217	-17	-20	-4	-287	875
	100.0%	4.3%	-15.9%	-1.2%	-1.5%	-0.3%	-21.1%	64.2%

From the Theoretical Max generation baseline an Array, AC and Grid & Curtailement Breakdown losses are seen accounting for most of the technical reduction. Overall, 64.2% of actual generation is achieved of theoretical max numbers.

Inverter Performance Report: Edinburgh

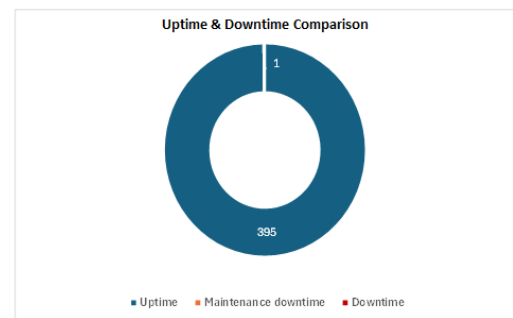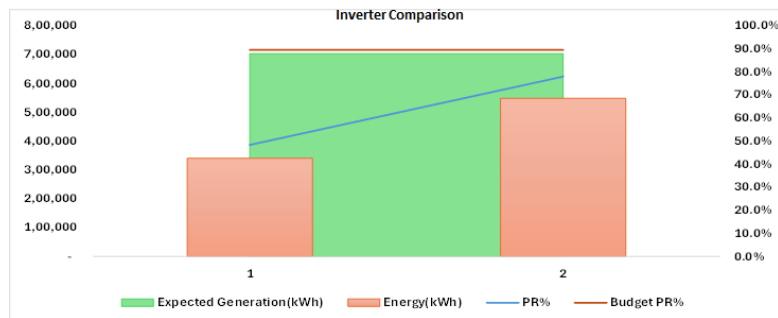

Top 5 Inverters

InverterName	PR%	Yield
I02	78.0%	112.6

Bottom 5 Inverters

InverterName	PR%	Yield
I01	48.4%	69.8

Downtime Details

1. Maintenance: NA
2. Downtime: 1 day, Impact: 4.0MWh

Technical Summary

This report highlights operational areas impacting site performance. Key concerns include radiation deficit, inverter underperformance, and a high share of unforeseen losses. These should be prioritized for diagnostic review.
